

Project Tracking & Rollup DASHBOARD


Project Name EPDP: Internationalized Domain Names **Program** gTLD **Project Sponsor** GNSO Council

Project Information


05/20/21
Current Start

08/18/23
Current Finish

41%
% Complete

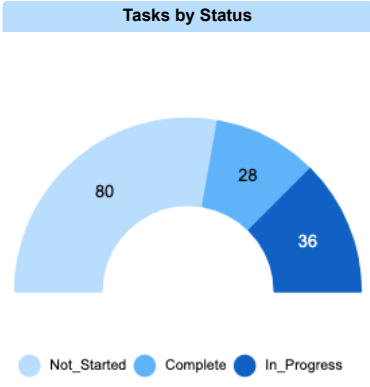

- Project Contacts**
- Donna Austin**
Chair
 - Justine Chew**
Vice_Chair
 - Farell Folly**
Liaison
 - Ariel Liang**
Staff_Lead
 - Steve Chan**
Project_Manager

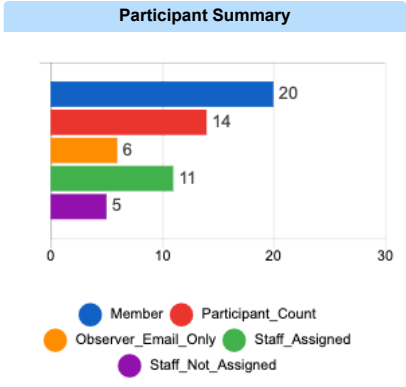

Project Status & Health

Project_Status	Project_Health
On-Schedule	On-Target

Summary Gantt & Key Milestones

Health	Primary Task	Current Start	Current Finish	% Complete	Status	Gantt Chart (2021-2023)											
	EPDP: Internationalized Domain Names	05/20/21	08/18/23	41%	In Progress	[Gantt bar for EPDP: Internationalized Domain Names]											
	PROJECT CONTROL	05/20/21	07/10/23	58%	In Progress	[Gantt bar for PROJECT CONTROL]											
	GROUP DELIBERATIONS	08/11/21	03/16/23	46%	In Progress	[Gantt bar for GROUP DELIBERATIONS]											
●	Group 1	08/25/21	02/17/22	87%	In Progress	[Gantt bar for Group 1]											
●	Group 2	02/04/22	03/31/22	65%	In Progress	[Gantt bar for Group 2]											
●	Group 3	03/18/22	06/02/22	8%	In Progress	[Gantt bar for Group 3]											
●	Group 4	05/20/22	08/04/22			[Gantt bar for Group 4]											
●	Group 5	07/22/22	09/16/22			[Gantt bar for Group 5]											
●	Group 6	09/05/22	10/24/22			[Gantt bar for Group 6]											
●	Group 7	10/11/22	11/11/22			[Gantt bar for Group 7]											
	INITIAL REPORT	09/20/21	02/03/23	24%	In Progress	[Gantt bar for INITIAL REPORT]											
	Publish Initial Report	12/16/22	12/16/22			[Milestone for Publish Initial Report]											
	Public comment forum on the Initial Report (40 days)	12/19/22	02/03/23			[Milestone for Public comment forum on the Initial Report (40 days)]											
	FINAL REPORT	02/06/23	04/07/23		Not Started	[Gantt bar for FINAL REPORT]											
	Review of public comments	02/06/23	03/17/23			[Milestone for Review of public comments]											
	Submission of Final Report to the GNSO Council	04/07/23	04/07/23			[Milestone for Submission of Final Report to the GNSO Council]											

4 - Working Group

Title:	EPDP - Internationalized Domain Names (EPDP_IDN)
Description & Scope:	On 20 May 2021, the GNSO Council passed a resolution to initiate the Expedited Policy Development Process (EPDP) on Internationalized Domain Names and adopt its charter. The EPDP Team is tasked with providing the GNSO Council with policy recommendations on: 1) the definition of gTLDs and the management of variant labels; and 2) how the IDN Implementation Guidelines, which Contracted Parties are required to comply with, should be updated in the future.

Composition:

Chair:	Donna Austin
Vice Chair:	Justine Chew
Council Liaison:	Farell Folly
Policy Staff:	A. Liang, S. Chan, E. Barabas.
GDS Staff:	S. Hussain, M. Karakash
# Participants:	34 Participants (link)
# Observers:	11
Tools:	Mailing List / Meeting Schedule / Wiki
Charter:	Charter

Project Management:

Token Holder	Planned Start Date	Actual Start Date	# of Days	Planned End Date	Actual End Date
WG	20 May 2021	20 May 2021	364	09 Jun 2023	TBD

Program	Progress	Status	Health
gTLD	41%	●	■

STATUS: ■ Planned ● On-schedule ● Revised schedule ▲ Behind schedule ◆ Target will be missed ■ On-hold

HEALTH: ■ On-Target ■ At-Risk ■ In-Trouble

Milestones/Work plan (link):

Milestone/Task	Date	
Project Start	May-21	✓
Scoping Team Report	Jan-20	✓
Charter Approved	May-21	✓
EPDP Initiation Request Approved	May-21	✓
1st Plenary meeting	Aug-21	✓
SO/AC & SG/C Input to PDP	Nov-21	✓
Project Plan and Work plan Adoption	Oct-21	✓
Issue Deliberations	Mar-23	
Populate draft report w/ findings & potential recs.	Oct-22	
Assemble initial conclusions	Oct-22	
Discuss/approve findings and interim recs.	Nov-22	
Consolidate interim recommendations and findings	Nov-22	
Issue report for public comment	Dec-22	
Review public comment input & prepare final report	Mar-23	
Finalize Report	Apr-23	
Determine consensus levels on recommendations	Apr-23	
Adopt final recommendations and report	Apr-23	
Send final report to GNSO Council	Apr-23	
GNSO Council adoption of consensus recs.	May-23	
Issue public comment for Board consideration	Jun-23	
ICANN Board adoption of consensus recs.	Oct-23	
Prior period % Complete	39%	

Status/Health Rationale:

- This project was initiated on 20 May 2021 and continues with a Status of “On-Schedule” and Health of “On-Target”

Current Activities:

- Conducting the first pass of substantive deliberations on Group 3 charter questions related to objection processes, string similarity review, string contention resolution, reserved strings, and other policies and procedures, as impacted by variant labels.
- Seeking input from Chinese, Japanese, and Korean Generation Panels regarding charter question A7 – the mechanism or criteria for identifying allowable characters for single-character TLDs in Han script.
- Seeking input from eligible Arabic and Chinese TLD registry operators regarding their potential interest in activating allocatable variants of their TLDs.

Planned Activities:

- Complete the first pass of substantive deliberations on Group 3 related to the objection processes, string similarity review, string contention resolution, reserved strings, and other policies and procedures, as impacted by variant labels.
- Conduct strawman analysis to understand which aspects of the New gTLD Program will be impacted due to the implementation of variants.
- Begin initial deliberations on Group 4 charter questions related to the “same entity” principle at the second-level.

Open Issues, Risks & Mitigation Plan:

- The EPDP-Team changed the sequencing of tackling charter questions to ensure that a logical order is being followed and provide efficiencies to deliberations. Deliberations of certain Charter questions also depend on the critical input from external parties, such as the Chinese/Japanese/Korean Generation Panels as well as Arabic and Chinese gTLD registry operators. Leadership intends to revisit the project plan to assess whether the original planning assumptions were reasonable, while factoring in the time needed for seeking external input. Council will be informed if any changes to the timing of milestones are considered necessary.
- At the time the Charter was developed, it was assumed that the SubPro recommendations, particularly those relating to IDNs under Topic 25, would have been approved by the ICANN Board. The IDN EPDP is conducting its work with the expectation that the SubPro recommendations will be approved by the Board at some future date. However, it has been necessary for the EPDP Team to make assumptions about the implementation of those recommendations in order to address the Charter questions. While these assumptions are believed to be sound, the Council should be aware of the possible ripple effect or potential risk to the EPDP Teamwork in the event that the Board does not adopt the related SubPro recommendations.

Completed in prior period(s):

- Completed the first pass of substantive deliberations on Group 1 charter questions related to the definition of all gTLDs using the Root Zone Label Generation Rules (RZ-LGR) ; reviewed draft outcome language developed for seven out of ten questions.
- Completed the first pass of deliberations of seven out of nine charter questions in Group 2 related to the “same entity” principle at the top-level.
- Received an update on ccPDP4’s deliberation on ccTLD variant definition and management.
- Completed and distributed [Project Package](#) for April.

Project Tracking & Rollup DASHBOARD




Project Roster

Participant	Participant Type	Role	Participation Start Date	Participation End Date	Legacy SOI Link
Group Selected / Nominated By: Group Name At-Large Advisory Committee (ALAC)					
Justine Chew	Participant	Vice-chair	05/25/21		https://community.icann.org
TV Gopal	Participant		05/25/21	03/21/22	https://community.icann.org
Hadia Elminiawi	Participant		07/14/21		https://community.icann.org
Satish Babu	Member		05/25/21		https://community.icann.org
Lianna Galstyan	Member		05/25/21		https://community.icann.org
Abdulkarim Oloyede	Member		05/25/21		https://community.icann.org
Group Selected / Nominated By: Group Name Commercial Business Users Constituency (BC)					
Mark William Datysgeld	Member		05/25/21		https://community.icann.org
Group Selected / Nominated By: Group Name Expedited Policy Development Process - IDNs					
Donna Austin	Member	Chair	08/10/21		https://community.icann.org
Group Selected / Nominated By: Group Name GNSO Council					
Ekue Farell Folly	Member	Liaison	07/27/21		https://community.icann.org
Group Selected / Nominated By: Group Name Governmental Advisory Committee (GAC)					
Hamza Onoruoiza Salami	Participant		05/25/21		https://community.icann.org
T. Santhosh	Member		05/25/21		https://community.icann.org
Nigel Hickson	Member		07/12/21		https://community.icann.org
Group Selected / Nominated By: Group Name ICANN Board					
Edmon Chung	Member	Liaison	07/27/21		https://community.icann.org
Akinori Maemura	Member	Liaison	11/18/21		https://community.icann.org
Group Selected / Nominated By: Group Name Independent					
Abdalmonem Galila	Participant		05/25/21		https://community.icann.org
Gao Lei	Participant		05/25/21		https://community.icann.org
Nabil Benamar	Participant		05/25/21		https://community.icann.org
Lisa Liang	Participant		05/25/21		https://community.icann.org
Anil Jain	Participant		07/30/21		https://community.icann.org
Quoc Pham	Participant		08/13/21		https://community.icann.org
Kenny Huang	Guest		10/26/21	10/26/21	
Group Selected / Nominated By: Group Name Intellectual Property Constituency (IPC)					
Brian King	Member		05/25/21	11/08/21	https://community.icann.org
Jeffrey Neuman	Member		05/25/21		https://community.icann.org
Group Selected / Nominated By: Group Name Internet Corporation for Assigned Names & Numbers (ICANN)					
Michael Karakash	Staff - Assigned	Liaison	05/25/21		
Steve Chan	Staff - Assigned		05/25/21		
Emily Barabas	Staff - Assigned		05/25/21		
Terri Agnew	Staff - Assigned		05/25/21		
Sarmad Hussain	Staff - Assigned	Liaison	05/25/21		
Nathalie Peregrine	Staff - Assigned		05/25/21		
Pitinan Kooarmornpatana	Staff - Assigned		05/25/21		
Ariel Liang	Staff - Assigned		05/25/21		
Julie Bisland	Staff - Assigned		05/25/21		
Michelle DeSmyter	Staff - Assigned		08/18/21		
Devan Reed	Staff - Assigned		12/02/21		
Group Selected / Nominated By: Group Name Internet Service Providers and Connectivity Providers Constituency (ISPCP)					
Christian Dawson	Participant		07/12/21		https://community.icann.org
Group Selected / Nominated By: Group Name Non-Commercial Stakeholder Group (NCSG)					
Tomslin Samme-Nlar	Member		05/25/21		https://community.icann.org
Akinremi Peter Taiwo	Member		07/15/21		https://community.icann.org
Group Selected / Nominated By: Group Name Registrar Stakeholder Group (RrSG)					
Michael Bauland	Member		05/25/21		https://community.icann.org
Duwei Chen	Member		09/26/21	02/13/22	https://community.icann.org
Zhang Zuan	Member		02/14/22		https://community.icann.org
Group Selected / Nominated By: Group Name Registry Stakeholder Group (RySG)					


Jennifer Chung	Participant		05/25/21		https://community.icann.org
Jerry Sen	Participant		05/25/21		https://community.icann.org
Wei (Wesley) Wang	Participant		07/13/21		https://community.icann.org
Maxim Alzoba	Member		05/25/21		https://community.icann.org
Joseph Chiu-Kit Yee	Member		07/06/21		https://community.icann.org
Dennis Tan Tanaka	Member		05/25/21		https://community.icann.org
<small>Group Selected / Nominated By: Group Name</small>					
Security and Stability Advisory Committee (SSAC)					
Lyman Chapin	Guest		01/13/22		
Jiankang Yao	Guest		01/13/22		
John R. Levine	Guest		01/13/22		
Ram Mohan	Guest		01/13/22		
Patrik Fältström	Guest		01/13/22		

Project Tracking & Rollup DASHBOARD


Work-Plan Activity Metrics

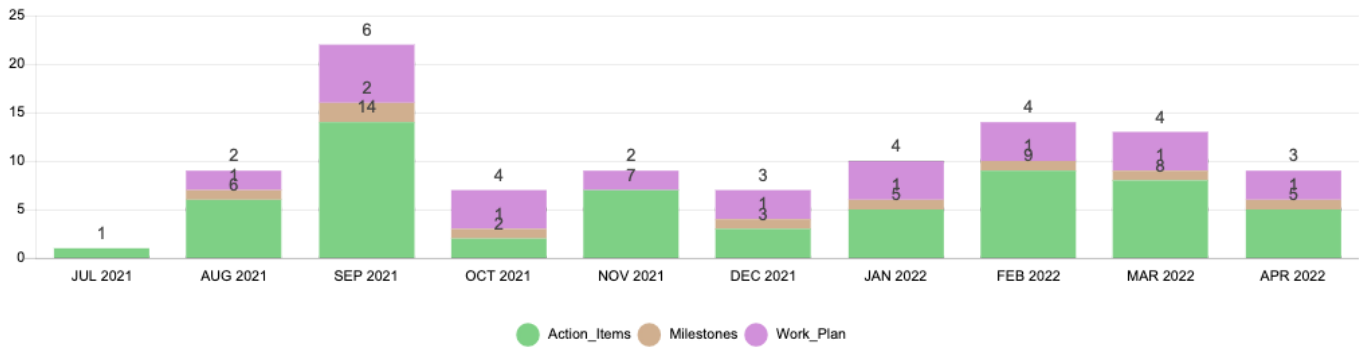

Mailman Activity

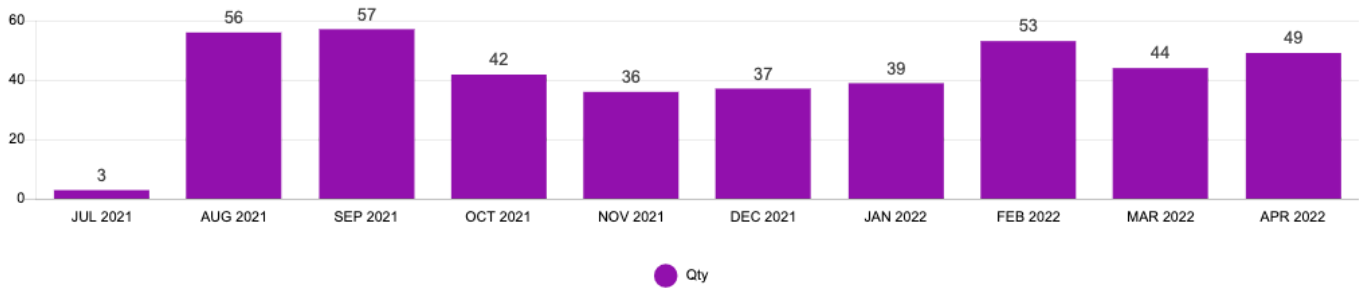

Meeting Activity

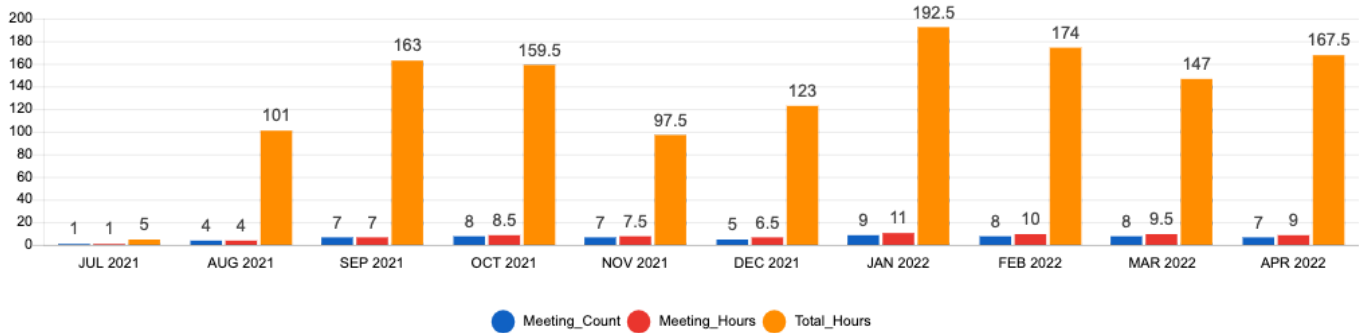

Plenary Attendance

Group Represented	Invited Qty	Attended Qty	Attendance
Total		Sum 1002	Sum 655 Avg 65.4%
Primary At-Large Advisory Committee (ALAC)		Sum 184	Sum 152 Avg 82.6%
Attendee Name Abdulkarim Oloyede		Sum 32	Sum 29 Avg 90.6%
Attendee Name Hadia Elminiawi		Sum 32	Sum 31 Avg 96.9%
Attendee Name Justine Chew		Sum 32	Sum 32 Avg 100.0%
Attendee Name Lianna Galstyan		Sum 32	Sum 24 Avg 75.0%
Attendee Name Satish Babu		Sum 32	Sum 30 Avg 93.8%
Attendee Name TV Gopal		Sum 24	Sum 6 Avg 25.0%
Primary Commercial Business Users Constituency (BC)		Sum 32	Sum 2 Avg 6.3%
Attendee Name Mark William Datysgeld		Sum 32	Sum 2 Avg 6.3%

Primary	Expedited Policy Development Process - IDNs	Sum	32	Sum	31	Avg	96.9%
Attendee Name	Donna Austin	Sum	32	Sum	31	Avg	96.9%
Primary	GNSO Council	Sum	32	Sum	24	Avg	75.0%
Attendee Name	Ekue Farell Folly	Sum	32	Sum	24	Avg	75.0%
Primary	Governmental Advisory Committee (GAC)	Sum	95	Sum	66	Avg	69.5%
Attendee Name	Hamza Onoruoza Salami	Sum	31	Sum	24	Avg	77.4%
Attendee Name	Nigel Hickson	Sum	32	Sum	23	Avg	71.9%
Attendee Name	T. Santhosh	Sum	32	Sum	19	Avg	59.4%
Primary	ICANN Board	Sum	50	Sum	48	Avg	96.0%
Attendee Name	Akinori Maemura	Sum	18	Sum	17	Avg	94.4%
Attendee Name	Edmon Chung	Sum	32	Sum	31	Avg	96.9%
Primary	Independent	Sum	185	Sum	73	Avg	39.5%
Attendee Name	Abdalmonem Galila	Sum	31	Sum	2	Avg	6.5%
Attendee Name	ANIL JAIN	Sum	32	Sum	26	Avg	81.3%
Attendee Name	Gao Lei	Sum	30	Sum	1	Avg	3.3%
Attendee Name	Kenny Huang	Sum	1	Sum	1	Avg	100.0%
Attendee Name	Lisa Liang	Sum	32	Sum	31	Avg	96.9%
Attendee Name	Nabil Benamar	Sum	30	Sum	0	Avg	0.0%
Attendee Name	Quoc Pham	Sum	29	Sum	12	Avg	41.4%
Primary	Intellectual Property Constituency (IPC)	Sum	45	Sum	35	Avg	77.8%
Attendee Name	Brian King	Sum	13	Sum	10	Avg	76.9%
Attendee Name	Jeffrey Neuman	Sum	32	Sum	25	Avg	78.1%
Primary	Internet Service Providers and Connectivity Providers Constituency (ISPCP)	Sum	31	Sum	10	Avg	32.3%
Attendee Name	Christian Dawson	Sum	31	Sum	10	Avg	32.3%
Primary	Non-Commercial Stakeholder Group (NCSG)	Sum	64	Sum	17	Avg	26.6%
Attendee Name	Akinremi Peter Taiwo	Sum	32	Sum	8	Avg	25.0%
Attendee Name	Tomslin Samme-Nlar	Sum	32	Sum	9	Avg	28.1%
Primary	Registrar Stakeholder Group (RrSG)	Sum	57	Sum	50	Avg	87.7%
Attendee Name	Duowei Chen	Sum	16	Sum	11	Avg	68.8%
Attendee Name	Michael Bauland	Sum	32	Sum	30	Avg	93.8%
Attendee Name	Zhang Zuan	Sum	9	Sum	9	Avg	100.0%
Primary	Registry Stakeholder Group (RySG)	Sum	190	Sum	142	Avg	74.7%
Attendee Name	Dennis Tan Tanaka	Sum	32	Sum	30	Avg	93.8%
Attendee Name	Jennifer Chung	Sum	31	Sum	24	Avg	77.4%
Attendee Name	Jerry Sen	Sum	32	Sum	32	Avg	100.0%
Attendee Name	Joseph Chiu-Kit Yee	Sum	32	Sum	29	Avg	90.6%
Attendee Name	Maxim Alzoba	Sum	32	Sum	24	Avg	75.0%

Attendee Name Wei (Wesley) Wang	Sum 31	Sum 3	Avg 9.7%
Primary Security and Stability Advisory Committee (SSAC)	Sum 5	Sum 5	Avg 100.0%
Attendee Name Jiankang Yao	Sum 1	Sum 1	Avg 100.0%
Attendee Name John R. Levine	Sum 1	Sum 1	Avg 100.0%
Attendee Name Lyman Chapin	Sum 1	Sum 1	Avg 100.0%
Attendee Name Patrik Fältström	Sum 1	Sum 1	Avg 100.0%
Attendee Name Ram Mohan	Sum 1	Sum 1	Avg 100.0%

[Open source report to view more](#)

Health	Task Name	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Status	Baseline Start	Baseline Finish	Q1			Q2			Q3			Q4			Q1			Q2			Q3														
										Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep
1	EPDP: Internationalized Domain Names	587d	05/20/21	08/18/23		41%	In Progress	05/20/21	08/18/23																																	
2	PROJECT CONTROL	558d	05/20/21	07/10/23		58%	In Progress	05/20/21	07/10/23																																	
3	Project start confirmed	0	05/20/21	05/20/21		100%	Complete	05/20/21	05/20/21																																	
4	Adopt/Confirm charter	0	05/20/21	05/20/21	3	100%	Complete	05/20/21	05/20/21																																	
5	Confirmation of Team	60d	05/20/21	08/11/21	3	100%	Complete	05/20/21	08/11/21																																	
6	Appointment of Team Chair	46d	05/20/21	07/22/21	3	100%	Complete	05/20/21	07/22/21																																	
7	Appointment of Liaison to GNSO Council	46d	05/20/21	07/22/21	3	100%	Complete	05/20/21	07/22/21																																	
8	Chair / Staff preparations	13d	07/23/21	08/10/21	6	100%	Complete	07/23/21	08/10/21																																	
9	Project Management	512d	07/23/21	07/10/23		44%	In Progress	07/23/21	07/10/23																																	
10	Develop and confirm Project Plan	50d	07/23/21	09/30/21	6	100%	Complete	07/23/21	09/30/21																																	
11	Obtain project plan approval from GNSO Council	20d	10/01/21	10/28/21	10	100%	Complete	10/01/21	10/28/21																																	
12	Develop monthly Project Packages and deliver to Group & Council	370d	10/29/21	03/30/23	11	30%	In Progress	10/29/21	03/30/23																																	
13	Leadership Sub team	440d	07/23/21	03/30/23		46%	In Progress	07/23/21	03/30/23																																	
14	On-going preparation and planning of group activities	440d	07/23/21	03/30/23	6	46%	In Progress	07/23/21	03/30/23																																	
15	Close project and transition project to implementation	1d	07/10/23	07/10/23	14, 164	0%	Not Started	07/10/23	07/10/23																																	
16	GROUP DELIBERATIONS	417d	08/11/21	03/16/23		46%	In Progress	08/11/21	03/16/23																																	
17	First meeting of Team	1d	08/11/21	08/11/21	8	100%	Complete	08/11/21	08/11/21																																	
18	Understand Charter, organize materials and develop initial approach	10d	08/11/21	08/24/21	8	100%	Complete	08/11/21	08/24/21																																	
19	Overview & initial discussion of all Policy Topics	10d	08/11/21	08/24/21	8	100%	Complete	08/11/21	08/24/21																																	
20	Develop definitions and terminology	28d	08/11/21	09/17/21	8	100%	Complete	08/11/21	09/17/21																																	
21	Input from other SO/ACs & GNSO SG/Cs	58d	09/09/21	11/29/21		100%	Complete	09/09/21	12/01/21																																	
26	Group 1	127d	08/25/21	02/17/22		86%	In Progress	08/25/21	11/02/21																																	
44	Group 2	40d	02/04/22	03/31/22		65%	In Progress	11/03/21	12/28/21																																	
58	Group 3	55d	03/18/22	06/02/22		8%	In Progress	12/29/21	02/22/22																																	
74	Group 4	55d	05/20/22	08/04/22				02/23/22	05/24/22																																	
88	Group 5	41d	07/22/22	09/16/22				05/25/22	08/02/22																																	
101	Group 6	36d	09/05/22	10/24/22				08/03/22	09/27/22																																	
111	Group 7	24d	10/11/22	11/11/22				09/28/22	11/04/22																																	
120	Unplanned Issues & Tasks	0	08/24/21	08/24/21				08/24/21	08/24/21																																	
137	Key Group Events	364d	10/25/21	03/16/23		39%	In Progress	10/25/21	03/16/23																																	
144	INITIAL REPORT	360d	09/20/21	02/03/23		24%	In Progress	09/20/21	02/03/23																																	
145	Populate stable drafts as required	300d	09/20/21	11/11/22	20	30%	In Progress	09/20/21	11/11/22																																	
146	Discuss/approve findings and interim recommendations	10d	11/14/22	11/25/22	145			11/14/22	11/25/22																																	
147	Consolidate interim recommendations and findings	10d	11/28/22	12/09/22	146			11/28/22	12/09/22																																	
148	Build Draft Report for public comment	10d	11/28/22	12/09/22	146			11/28/22	12/09/22																																	
149	Approve Draft Report for public comment	5d	12/12/22	12/16/22	148			12/12/22	12/16/22																																	
150	Publish Initial Report	0	12/16/22	12/16/22	149			12/16/22	12/16/22																																	
151	Communicate Initial Report	5d	12/19/22	12/23/22	149			12/19/22	12/23/22																																	
152	Public comment forum on the Initial Report (40 days)	35d	12/19/22	02/03/23	149			12/19/22	02/03/23																																	
153	FINAL REPORT	45d	02/06/23	04/07/23			Not Started	02/06/23	04/07/23																																	
154	Review of public comments	30d	02/06/23	03/17/23	152			02/06/23	03/17/23																																	
155	Continue deliberations of policy topics towards a Final Report	30d	02/06/23	03/17/23	152			02/06/23	03/17/23																																	
156	Build Final Report & Final Deliberations	5d	03/20/23	03/24/23	155			03/20/23	03/24/23																																	
157	Determine consensus levels on interim recommendations	10d	03/27/23	04/07/23	156			03/27/23	04/07/23																																	
158	Adopt final recommendations and report	10d	03/27/23	04/07/23	156			03/27/23	04/07/23																																	
159	Submission of Final Report to the GNSO Council	0	04/07/23	04/07/23	158			04/07/23	04/07/23																																	
160	POST GROUP TASKS	95d	04/10/23	08/18/23			Not Started	04/10/23	08/18/23																																	
165																																										
166	PDP CHECKLIST	99d	01/01/21	05/20/21																																						

Health	Category	Action Item	Priority	Assigned To	Baseline Finish	Current Finish	Status	Notes
	WP	Meeting #29 B4a, B5, A7, A10	↓	EPDP_IDN	04/07/22	04/07/22	Complete	
	MS	Submit project package to GNSO Council	!	Policy Support Staff	04/05/22	04/05/22	Complete	
	AI	Action Item 1: RySG members on the EPDP Team to ask geoTLD colleagues if they have any concerns about the direction that the group is taking on charter question B5.	—	EPDP_IDN	04/30/22	04/30/22	Complete	
	AI	Action Item 2: Leadership Team to draft response to charter question B5 and recommendation.	—	Policy Support Staff	04/14/22	04/14/22	Complete	
	AI	Action Item 3: Leadership Team to send proposed approach to outreach to CJK GPs to the EPDP Team for review and response on the mailing list, to be wrapped up next week. The EPDP Team will try to raise and resolve questions on email.	—	Policy Support Staff	04/04/22	04/04/22	Complete	
●	AI	Action Item 4: Leadership Team to send follow-up email regarding proposed outcome for Charter question A10.	—	Policy Support Staff	05/05/22		In Progress	
	WP	Meeting #30 B4a, B5, A7, A10	↓	EPDP_IDN	04/14/22	04/07/22	Complete	
	AI	Action Item 1: Leadership team to come back with ideas about how to break down the problem set for E1 and E3.	—	EPDP_IDN Leadership Policy Support Staff	04/21/22	04/21/22	Complete	
	AI	Action Item 2: Leadership team and staff to consider next steps on data collection regarding variants of reserved names, including blocked variants.	—	Policy Support Staff	04/28/22	04/26/22	Complete	
	WP	Meeting #31 E3, E1 (Part 1), E3a, E5	↓	EPDP_IDN	04/28/22	04/14/22	Complete	
	AI	Action Item 1: Staff to proceed with next steps on distributing questions to ROs that have new gTLDs in Chinese and Arabic scripts.	—	Policy Support Staff	05/12/22		In Progress	
	AI	Action Item 2: Staff to request volunteers to join a small group tasked with developing examples related to Levels 1, 2, and 3. Staff to circulate a doodle to find a time for the small group to meet.	—	Policy Support Staff	05/06/22		In Progress	
●	WP	Meeting #32 E5, E2, E1 (Part 2), E4	↓	EPDP_IDN	05/05/22		Not Started	
	WP	Meeting #33 TBD	↓	EPDP_IDN	05/12/22		Not Started	
●	WP	Meeting #34 TBD	↓	EPDP_IDN	05/05/22		Not Started	
	MS	Submit project package to GNSO Council	!	Ariel Liang	05/06/22		Not Started	
	WP	Meeting #35 TBD	↓	EPDP_IDN	05/12/22		Not Started	
	WP	Meeting #36 TBD	↓	EPDP_IDN	05/19/22		Not Started	
	WP	Meeting #37 TBD	↓	EPDP_IDN	05/26/22		Not Started	
	WP	Meeting #38 TBD	↓	EPDP_IDN	06/02/22		Not Started	
	MS	Submit project package to GNSO Council	!	Ariel Liang	06/03/22		Not Started	
	WP	Meeting #39 TBD	↓	EPDP_IDN	06/09/22		Not Started	
	WP	Meeting ICANN74 TBD	↓	EPDP_IDN	06/14/22		Not Started	
	WP	Meeting #40 TBD	↓	EPDP_IDN	06/16/22		Not Started	
	MS	Submit project package to GNSO Council	!	Ariel Liang	07/08/22		Not Started	
