

Project Tracking & Rollup DASHBOARD

Project Name EPDP: Internationalized Domain Names **Program** IDNs **Project Sponsor** GNSO Council


Project Information

05/20/21
Current Start

03/20/26
Current Finish

26%
% Complete

Tasks by Status



● Not_Started ● Complete ● In_Progress

Project Contacts

Donna Austin
Chair


Justine Chew
Vice_Chair

Farell Folly
Liaison

AL Ariel Liang
Staff_Lead

SC Steve Chan
Project_Manager

Participant Summary



● Member ● Participant_Count
● Observer_Email_Only ● Staff_Assigned
● Staff_Not_Assigned

Project Status & Health

Project_Status: Behind Schedule Project_Health: On-Target

Summary Gantt & Key Milestones																													
Health	Primary Task	Current Start	Current Finish	% Complete	Status	Timeline (2021-2025)																							
						2021		2022		2023			2024			2025													
						Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
	EPDP: Internationalized Domain Names	05/20/21	03/20/26	26%	In Progress	[Gantt bar spanning from Q1 2021 to Q4 2025]																							
	PROJECT CONTROL	05/20/21	02/09/26	39%	In Progress	[Gantt bar spanning from Q1 2021 to Q4 2025]																							
	GROUP DELIBERATIONS	08/11/21	10/30/25	33%	In Progress	[Gantt bar spanning from Q3 2021 to Q4 2025]																							
●	Group 1: Definition of All gTLDs Using RZ-LGR	08/25/21	02/17/22	99%	In Progress	[Gantt bar spanning from Q3 2021 to Q4 2025]																							
●	Group 2: Same Entity at Top-Level	02/04/22	03/31/22	87%	In Progress	[Gantt bar spanning from Q1 2022 to Q4 2025]																							
	Group 3: Objection Processes, String Similarity Review, String Contention Resolution, Reserved Strings, and Other Policies and Procedures as Impacted by Variants	03/18/22	01/06/23	55%	In Progress	[Gantt bar spanning from Q2 2022 to Q4 2025]																							
	Data Collection to Facilitate Phase 2 Deliberations	11/07/22	07/07/23	0%	In Progress	[Gantt bar spanning from Q4 2022 to Q4 2025]																							
	Group 4: Same Entity at Second-Level	11/06/23	03/29/24	11%	In Progress	[Gantt bar spanning from Q4 2023 to Q4 2025]																							
	Group 5: Domain Name Lifecycle	04/01/24	08/23/24			[Gantt bar spanning from Q1 2024 to Q4 2025]																							
	Group 6: Registration Dispute Resolution Procedures and Trademark Protection Mechanisms	08/26/24	10/25/24			[Gantt bar spanning from Q3 2024 to Q4 2025]																							
	Group 7: IDN Implementation Guidelines	10/28/24	01/03/25			[Gantt bar spanning from Q4 2024 to Q4 2025]																							
	INITIAL REPORT	09/20/21	06/13/25	21%	In Progress	[Gantt bar spanning from Q3 2021 to Q4 2025]																							
	Phase 1 Initial Report	09/20/21	06/09/23	41%	In Progress	[Gantt bar spanning from Q3 2021 to Q4 2025]																							
	Publish Phase 1 Initial Report	04/21/23	04/21/23			[Milestone diamond at Q2 2023]																							
	Public comment forum on Phase 1 Initial Report (40 days)	04/24/23	06/09/23			[Gantt bar spanning from Q2 2023 to Q4 2025]																							
	Phase 2 Initial Report	11/13/23	06/13/25			[Gantt bar spanning from Q4 2023 to Q4 2025]																							
	Public comment forum on Phase 2 Initial Report (40 days)	04/28/25	06/13/25			[Gantt bar spanning from Q1 2025 to Q4 2025]																							
	FINAL REPORT	06/12/23	11/07/25		Not Started	[Gantt bar spanning from Q2 2023 to Q4 2025]																							
	Review of public comments	06/12/23	07/21/23			[Gantt bar spanning from Q2 2023 to Q4 2025]																							
	Submission of Phase 1 Final Report to the GNSO Council	11/03/23	11/03/23			[Milestone diamond at Q4 2023]																							
	Review of public comments	06/16/25	07/25/25			[Gantt bar spanning from Q2 2025 to Q4 2025]																							
	Submission of Phase 2 Final Report to the GNSO Council	11/07/25	11/07/25			[Milestone diamond at Q4 2025]																							

4 - Working Group

Title: EPDP - Internationalized Domain Names (EPDP_IDN)



Description & Scope: On 20 May 2021, the GNSO Council passed a resolution to initiate the Expedited Policy Development Process (EPDP) on Internationalized Domain Names and adopt its charter. The EPDP Team is tasked with providing the GNSO Council with policy recommendations on: 1) the definition of gTLDs and the management of variant labels; and 2) how the IDN Implementation Guidelines, which Contracted Parties are required to comply with, should be updated in the future.

Composition:

Chair:	Donna Austin
Vice Chair:	Justine Chew
Council Liaison:	Farell Folly
Policy Staff:	A. Liang, S. Chan, E. Barabas
GDS Staff:	S. Hussain, M. Karakash
# Participants:	36 Participants (link)
# Observers:	12
Tools:	Mailing List / Meeting Schedule / Wiki
Charter:	Charter

Project Management:

Token Holder	Planned Start Date	Actual Start Date	# of Days	Planned End Date	Actual End Date
WG	20 May 2021	20 May 2021	546	09 Jun 2023	TBD

Program	Progress	Status	Health
IDNs	26%		

STATUS: ■ Planned ● On-schedule ● Revised schedule ▲ Behind schedule ◆ Target will be missed ■ On-hold

HEALTH: ■ On-Target ■ At-Risk ■ In-Trouble

Milestones/Work plan (link):

Milestone/Task	Date	
Project Start	May-21	✓
Scoping Team Report	Jan-20	✓
Charter Approved	May-21	✓
EPDP Initiation Request Approved	May-21	✓
1st Plenary meeting	Aug-21	✓
SO/AC & SG/C Input to PDP	Nov-21	✓
Project Plan and Work plan Adoption	Oct-21	✓
Issue Deliberations	Mar-23	
Populate draft report w/ findings & potential recs.	Oct-22	
Assemble initial conclusions	Oct-22	
Discuss/approve findings and interim recs.	Nov-22	
Consolidate interim recommendations and findings	Nov-22	
Issue report for public comment	Dec-22	
Review public comment input & prepare final report	Mar-23	
Finalize Report	Apr-23	
Determine consensus levels on recommendations	Apr-23	
Adopt final recommendations and report	Apr-23	
Send final report to GNSO Council	Apr-23	
GNSO Council adoption of consensus recs.	May-23	
Issue public comment for Board consideration	Jun-23	
ICANN Board adoption of consensus recs.	Oct-23	
Prior period % Complete	56%	

Status/Health Rationale:

- This project Status was downgraded to “Behind Schedule” on 31 Aug 2022 and Health of “On-Target”.
- Note the percent complete listed above reflects the new proposed project schedule. The Status and Planned End Date will be reset after the GNSO Council’s consideration of the project change request.

Current Activities:

- Council consideration of the updated project plan and project change request.
- Wrapping up deliberations of charter questions related to top-level variant management.

Planned Activities:

- Consider ICANN org input on draft Phase 1 recommendations.
- Prepare public comment for the Phase 1 Initial Report, focusing on top-level variant management related recommendations.
- Conduct data collection among contracted parties to assist EPDP Team’s deliberation on second-level variant management related issues in Phase 2.

Open Issues & Risks:


- Deliberations of certain Charter questions depend on the critical input from external parties and additional data collection efforts.
- The EPDP Team plans to complete the work with a two-phased approach. Phase 1 focuses on top-level variant management related recommendations and Phase 2 focuses on second-level variant management. The EPDP Team plans to submit a project change request to the Council, seeking approval for the updated project plan.
- At the time the Charter was developed, it was assumed that the SubPro recommendations, particularly those relating to IDNs under Topic 25, would have been approved by the ICANN Board. The IDN EPDP is conducting its work with the expectation that the SubPro recommendations will be approved by the Board at some future date. However, it has been necessary for the EPDP Team to make assumptions about the implementation of those recommendations in order to address the Charter questions. While these assumptions are believed to be sound, the Council should be aware of the possible ripple effect or potential risk to the EPDP Teamwork in the event that the Board does not adopt the related SubPro recommendations.

Completed in prior period(s):


- Updated the project plan and developed a project change request to be submitted to the GNSO Council in November 2022, with a proposal of completing the EPDP in two phases.
- EPDP Team Chair Donna Austin provided the GNSO Council with a preview of its project change request during the October 2022 Council meeting.
- Sent a request to the Chinese, Japanese, and Korean Generation Panels to initiate work on identifying guidelines and/or a prohibitive list of Han characters that should not be allowed as single-character gTLDs.
- Completed and distributed [Project Package](#) for October.

Project Tracking & Rollup DASHBOARD


Work-Plan Activity Metrics

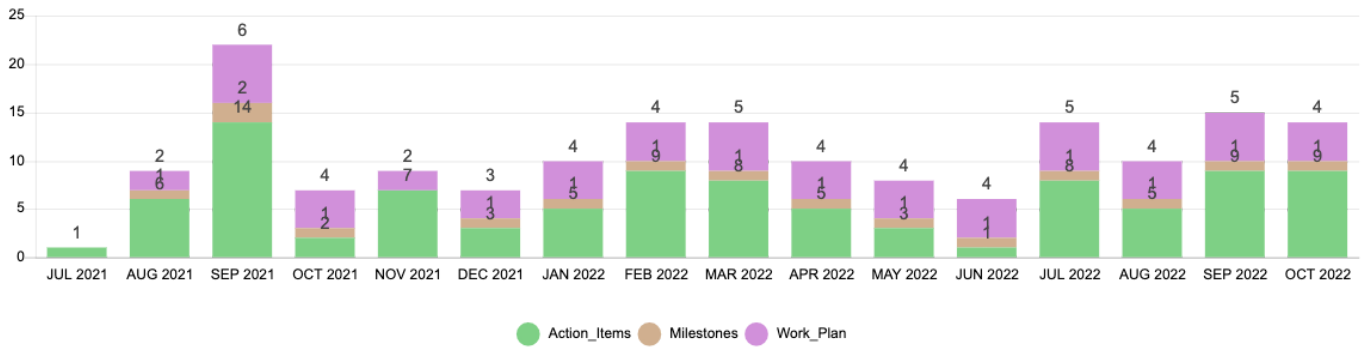

Mailman Activity

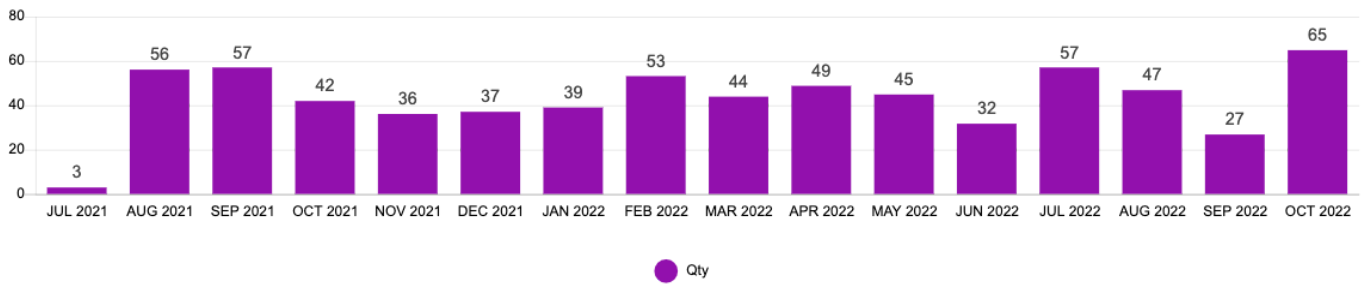

Meeting Activity

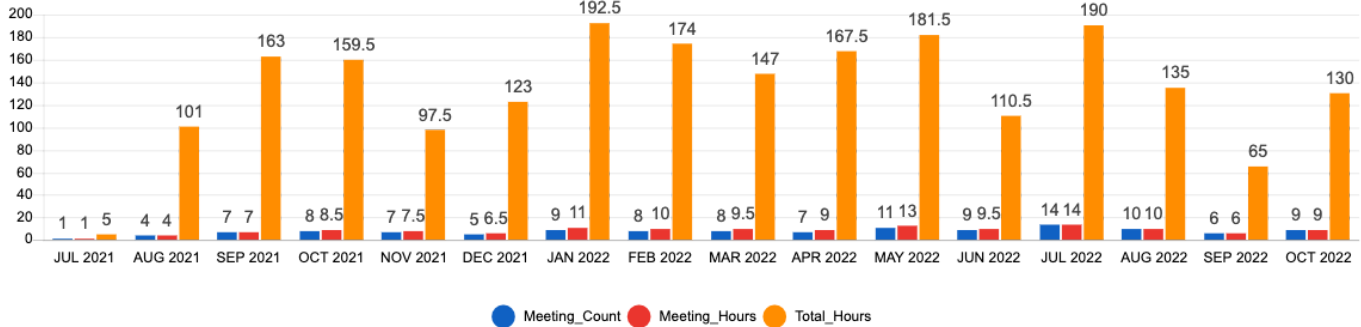

Plenary Attendance

Group Represented	Invited Qty	Attended Qty	Attendance
Total	Sum 1644	Sum 1009	Avg 61.4%
Primary At-Large Advisory Committee (ALAC)	Sum 287	Sum 232	Avg 80.8%
Attendee Name Abdulkarim Oloyede	Sum 52	Sum 43	Avg 82.7%
Attendee Name Hadia Elminiawi	Sum 53	Sum 52	Avg 98.1%
Attendee Name Justine Chew	Sum 53	Sum 53	Avg 100.0%
Attendee Name Lianna Galstyan	Sum 52	Sum 29	Avg 55.8%
Attendee Name Satish Babu	Sum 53	Sum 49	Avg 92.5%
Attendee Name TV Gopal	Sum 24	Sum 6	Avg 25.0%
Primary Commercial Business Users Constituency (BC)	Sum 34	Sum 2	Avg 5.9%
Attendee Name Mark William Datysgeld	Sum 34	Sum 2	Avg 5.9%

Primary	Sum	Sum	Avg
Expedited Policy Development Process - IDNs	53	50	94.3%
Attendee Name	Sum	Sum	Avg
Donna Austin	53	50	94.3%
Primary	Sum	Sum	Avg
GNSO Council	53	40	75.5%
Attendee Name	Sum	Sum	Avg
Ekue Farell Folly	53	40	75.5%
Primary	Sum	Sum	Avg
Governmental Advisory Committee (GAC)	155	89	57.4%
Attendee Name	Sum	Sum	Avg
Hamza Onoruoiza Salami	51	38	74.5%
Attendee Name	Sum	Sum	Avg
Nigel Hickson	52	31	59.6%
Attendee Name	Sum	Sum	Avg
T. Santhosh	52	20	38.5%
Primary	Sum	Sum	Avg
ICANN Board	88	76	86.4%
Attendee Name	Sum	Sum	Avg
Akinori Maemura	36	29	80.6%
Attendee Name	Sum	Sum	Avg
Edmon Chung	52	47	90.4%
Primary	Sum	Sum	Avg
Independent	340	117	34.4%
Attendee Name	Sum	Sum	Avg
Abdalmonem Galila	51	4	7.8%
Attendee Name	Sum	Sum	Avg
ANIL JAIN	52	42	80.8%
Attendee Name	Sum	Sum	Avg
Gao Lei	50	1	2.0%
Attendee Name	Sum	Sum	Avg
Imran Hossen	20	7	35.0%
Attendee Name	Sum	Sum	Avg
Kenny Huang	1	1	100.0%
Attendee Name	Sum	Sum	Avg
Lisa Liang	52	50	96.2%
Attendee Name	Sum	Sum	Avg
Nabil Benamar	50	0	0.0%
Attendee Name	Sum	Sum	Avg
Quoc Pham	49	12	24.5%
Attendee Name	Sum	Sum	Avg
Wael Nasr	15	0	0.0%
Primary	Sum	Sum	Avg
Intellectual Property Constituency (IPC)	65	44	67.7%
Attendee Name	Sum	Sum	Avg
Brian King	13	10	76.9%
Attendee Name	Sum	Sum	Avg
Jeffrey Neuman	52	34	65.4%
Primary	Sum	Sum	Avg
Internet Service Providers and Connectivity Providers Constituency (ISPCP)	51	17	33.3%
Attendee Name	Sum	Sum	Avg
Christian Dawson	51	17	33.3%
Primary	Sum	Sum	Avg
Non-Commercial Stakeholder Group (NCSG)	104	22	21.2%
Attendee Name	Sum	Sum	Avg
Akinremi Peter Taiwo	52	8	15.4%
Attendee Name	Sum	Sum	Avg
Emmanuel Vitus Agbenonwossi	13	5	38.5%
Attendee Name	Sum	Sum	Avg
Tomslin Samme-Nlar	39	9	23.1%
Primary	Sum	Sum	Avg
Registrar Stakeholder Group (RrSG)	99	87	87.9%
Attendee Name	Sum	Sum	Avg
Duowei Chen	16	11	68.8%
Attendee Name	Sum	Sum	Avg
Michael Bauland	53	47	88.7%
Attendee Name	Sum	Sum	Avg
Zhang Zuan	30	29	96.7%
Primary	Sum	Sum	Avg
Registry Stakeholder Group (RySG)	310	228	73.5%
Attendee Name	Sum	Sum	Avg
Dennis Tan Tanaka	52	48	92.3%
Attendee Name	Sum	Sum	Avg
Jennifer Chung	51	39	76.5%

Attendee Name Jerry Sen	Sum 52	Sum 51	Avg 98.1%
Attendee Name Joseph Chiu-Kit Yee	Sum 52	Sum 45	Avg 86.5%
Attendee Name Maxim Alzoba	Sum 52	Sum 42	Avg 80.8%
Attendee Name Wei (Wesley) Wang	Sum 51	Sum 3	Avg 5.9%
Primary Security and Stability Advisory Committee (SSAC)	Sum 5	Sum 5	Avg 100.0%
Attendee Name Jiankang Yao	Sum 1	Sum 1	Avg 100.0%
Attendee Name John R. Levine	Sum 1	Sum 1	Avg 100.0%
Attendee Name Lyman Chapin	Sum 1	Sum 1	Avg 100.0%
Attendee Name Patrik Fältström	Sum 1	Sum 1	Avg 100.0%
Attendee Name Ram Mohan	Sum 1	Sum 1	Avg 100.0%

Project Tracking & Rollup DASHBOARD



Project Roster

Participant	Participant Type	Role	Participation Start Date	Participation End Date	Legacy SOI Link
Group Selected / Nominated By: Group Name At-Large Advisory Committee (ALAC)					
Justine Chew	Participant	Vice-chair	05/25/21		https://community.icann.org
TV Gopal	Participant		05/25/21	03/21/22	https://community.icann.org
Hadia Elminiawi	Participant		07/14/21		https://community.icann.org
Satish Babu	Member		05/25/21		https://community.icann.org
Lianna Galstyan	Member		05/25/21		https://community.icann.org
Abdulkarim Oloyede	Member		05/25/21		https://community.icann.org
Group Selected / Nominated By: Group Name Commercial Business Users Constituency (BC)					
Mark William Datysgeld	Member		05/25/21	05/12/22	https://community.icann.org
Group Selected / Nominated By: Group Name Expedited Policy Development Process - IDNs					
Donna Austin	Member	Chair	08/10/21		https://community.icann.org
Group Selected / Nominated By: Group Name GNSO Council					
Ekue Farell Folly	Member	Liaison	07/27/21		https://community.icann.org
Group Selected / Nominated By: Group Name Governmental Advisory Committee (GAC)					
Hamza Onoruoiza Salami	Participant		05/25/21		https://community.icann.org
T. Santhosh	Member		05/25/21		https://community.icann.org
Nigel Hickson	Member		07/12/21		https://community.icann.org
Group Selected / Nominated By: Group Name ICANN Board					
Edmon Chung	Member	Liaison	07/27/21		https://community.icann.org
Akinori Maemura	Member	Liaison	11/18/21	09/22/22	https://community.icann.org
Group Selected / Nominated By: Group Name Independent					
Abdalmonem Galila	Participant		05/25/21		https://community.icann.org
Gao Lei	Participant		05/25/21		https://community.icann.org
Nabil Benamar	Participant		05/25/21		https://community.icann.org
Lisa Liang	Participant		05/25/21		https://community.icann.org
Anil Jain	Participant		07/30/21		https://community.icann.org
Quoc Pham	Participant		08/13/21		https://community.icann.org
Imran Hossen	Participant		11/04/21		https://community.icann.org
Wael Nasr	Participant		06/09/22		https://community.icann.org
Kenny Huang	Guest		10/26/21	10/26/21	
Group Selected / Nominated By: Group Name Intellectual Property Constituency (IPC)					
Brian King	Member		05/25/21	11/08/21	https://community.icann.org
Jeffrey Neuman	Member		05/25/21		https://community.icann.org
Group Selected / Nominated By: Group Name Internet Corporation for Assigned Names & Numbers (ICANN)					
Michael Karakash	Staff - Assigned	Liaison	05/25/21		
Steve Chan	Staff - Assigned		05/25/21		
Emily Barabas	Staff - Assigned		05/25/21		
Terri Agnew	Staff - Assigned		05/25/21		
Sarmad Hussain	Staff - Assigned	Liaison	05/25/21		
Nathalie Peregrine	Staff - Assigned		05/25/21		
Pitinan Kooarmompatana	Staff - Assigned		05/25/21		
Ariel Liang	Staff - Assigned		05/25/21		
Julie Bisland	Staff - Assigned		05/25/21		
Michelle DeSmyter	Staff - Assigned		08/18/21		
Devan Reed	Staff - Assigned		12/02/21		
Group Selected / Nominated By: Group Name Internet Service Providers and Connectivity Providers Constituency (ISPCP)					
Christian Dawson	Participant		07/12/21		https://community.icann.org
Group Selected / Nominated By: Group Name Non-Commercial Stakeholder Group (NCSG)					
Emmanuel Vitus Agbenonwossi	Member		07/13/22		https://community.icann.org
Akinremi Peter Taiwo	Member		07/15/21		https://community.icann.org
Group Selected / Nominated By: Group Name Registrar Stakeholder Group (RrSG)					
Michael Bauland	Member		05/25/21		https://community.icann.org
Duowei Chen	Member		09/26/21	02/13/22	https://community.icann.org
Zhang Zhan	Member		02/14/22		https://community.icann.org

Group Name	MEMBER	MEMBER	MEMBER	MEMBER	MEMBER
Group Selected / Nominated By: Group Name					
Registry Stakeholder Group (RySG)					
Jennifer Chung	Participant		05/25/21		https://community.icann.org
Jerry Sen	Participant		05/25/21		https://community.icann.org
Wei (Wesley) Wang	Participant		07/13/21		https://community.icann.org
Maxim Alzoba	Member		05/25/21		https://community.icann.org
Joseph Chiu-Kit Yee	Member		07/06/21		https://community.icann.org
Dennis Tan Tanaka	Member		05/25/21		https://community.icann.org
Group Selected / Nominated By: Group Name					
Security and Stability Advisory Committee (SSAC)					
Lyman Chapin	Guest		01/13/22		
Jiankang Yao	Guest		01/13/22		
John R. Levine	Guest		01/13/22		
Ram Mohan	Guest		01/13/22		
Patrik Fältström	Guest		01/13/22		

Health	Task Name	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Status	Baseline Start	Baseline Finish	2021				2022				2023				2024				2025				2026			
										Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
1	EPDP: Internationalized Domain Names	1262d	05/20/21	03/20/26		26%	In Progress	05/20/21	03/20/26																								
2	PROJECT CONTROL	1233d	05/20/21	02/09/26		39%	In Progress	05/20/21	02/09/26																								
3	Project start confirmed	0	05/20/21	05/20/21		100%	Complete	05/20/21	05/20/21																								
4	Adopt/Confirm charter	0	05/20/21	05/20/21	3	100%	Complete	05/20/21	05/20/21																								
5	Confirmation of Team	60d	05/20/21	08/11/21	3	100%	Complete	05/20/21	08/11/21																								
6	Appointment of Team Chair	46d	05/20/21	07/22/21	3	100%	Complete	05/20/21	07/22/21																								
7	Appointment of Liaison to GNSO Council	46d	05/20/21	07/22/21	3	100%	Complete	05/20/21	07/22/21																								
8	Chair / Staff preparations	13d	07/23/21	08/10/21	6	100%	Complete	07/23/21	08/10/21																								
9	Project Management	1187d	07/23/21	02/09/26		30%	In Progress	07/23/21	02/09/26																								
10	Develop and confirm Project Plan	50d	07/23/21	09/30/21	6	100%	Complete	07/23/21	09/30/21																								
11	Obtain project plan approval from GNSO Council	20d	10/01/21	10/28/21	10	100%	Complete	10/01/21	10/28/21																								
12	Develop monthly Project Packages and deliver to Group & Council	1050d	10/29/21	11/06/25	11	25%	In Progress	10/29/21	11/06/25																								
13	Leadership Sub team	1130d	07/23/21	11/20/25		30%	In Progress	07/23/21	11/20/25																								
14	On-going preparation and planning of group activities	1130d	07/23/21	11/20/25	6	30%	In Progress	07/23/21	11/20/25																								
15	Close project and transition project to implementation	1d	02/09/26	02/09/26	14, 179	0%		02/09/26	02/09/26																								
16	GROUP DELIBERATIONS	1102d	08/11/21	10/30/25		33%	In Progress	08/11/21	10/30/25																								
17	First meeting of Team	1d	08/11/21	08/11/21	8	100%	Complete	08/11/21	08/11/21																								
18	Understand Charter, organize materials and develop initial approach	10d	08/11/21	08/24/21	8	100%	Complete	08/11/21	08/24/21																								
19	Overview & initial discussion of all Policy Topics	10d	08/11/21	08/24/21	8	100%	Complete	08/11/21	08/24/21																								
20	Develop definitions and terminology	28d	08/11/21	09/17/21	8	100%	Complete	08/11/21	09/17/21																								
21	Input from other SO/ACs & GNSO SG/Cs	58d	09/09/21	11/29/21		100%	Complete	09/09/21	11/29/21																								
26	Phase 1 Deliberations	403d	08/25/21	03/10/23		64%	In Progress	08/25/21	03/10/23																								
27	Group 1: Definition of All gTLDs Using RZ-LGR	127d	08/25/21	02/17/22		99%	In Progress	08/25/21	02/17/22																								
44	Group 2: Same Entity at Top-Level	40d	02/04/22	03/31/22		87%	In Progress	02/04/22	03/31/22																								
58	Group 3: Objection Processes, String Similarity Review, String Contention Resolution, Reserved Strings, and Other Policies and Procedures as Impacted by Variants	211d	03/18/22	01/06/23		55%	In Progress	03/18/22	01/06/23																								
75	Review ICANN Org Input for Phase 1 Draft Recommendations	55d	12/26/22	03/10/23	72			12/26/22	03/10/23																								
76	Data Collection to Facilitate Phase 2 Deliberations	175d	11/07/22	07/07/23		0%	In Progress	11/07/22	07/07/23																								
77	Phase 2 Deliberations	355d	11/06/23	03/14/25		3%	In Progress	11/06/23	03/14/25																								
78	Group 4: Same Entity at Second-Level	105d	11/06/23	03/29/24		11%	In Progress	11/06/23	03/29/24																								
92	Group 5: Domain Name Lifecycle	105d	04/01/24	08/23/24				04/01/24	08/23/24																								
106	Group 6: Registration Dispute Resolution Procedures and Trademark Protection Mechanisms	45d	08/26/24	10/25/24				08/26/24	10/25/24																								
116	Group 7: IDN Implementation Guidelines	50d	10/28/24	01/03/25				10/28/24	01/03/25																								
125	Review ICANN Org Input for Phase 2 Draft Recommendations	50d	01/06/25	03/14/25	124			01/06/25	03/14/25																								
126	Key Group Events	1049d	10/25/21	10/30/25		30%	In Progress	10/25/21	10/30/25																								
141	INITIAL REPORT	975d	09/20/21	06/13/25		21%	In Progress	09/20/21	06/13/25																								
142	Phase 1 Initial Report	450d	09/20/21	06/09/23		41%		09/20/21	06/09/23																								
143	Populate stable drafts as required	385d	09/20/21	03/10/23	20	50%	In Progress	09/20/21	03/10/23																								
144	Discuss/approve findings and interim recommendations	15d	03/13/23	03/31/23	143			03/13/23	03/31/23																								
145	Consolidate interim recommendations and findings	10d	04/03/23	04/14/23	144			04/03/23	04/14/23																								
146	Build Draft Report for public comment	10d	04/03/23	04/14/23	144			04/03/23	04/14/23																								
147	Approve Draft Report for public comment	5d	04/17/23	04/21/23	146			04/17/23	04/21/23																								
148	Publish Phase 1 Initial Report	0	04/21/23	04/21/23	147			04/21/23	04/21/23																								
149	Communicate Phase 1 Initial Report	5d	04/24/23	04/28/23	147			04/24/23	04/28/23																								
150	Public comment forum on Phase 1 Initial Report (40 days)	35d	04/24/23	06/09/23	147			04/24/23	06/09/23																								
151	Phase 2 Initial Report	415d	11/13/23	06/13/25				11/13/23	06/13/25																								
152	Populate stable drafts as required	350d	11/13/23	03/14/25	80			11/13/23	03/14/25																								
153	Discuss/approve findings and interim recommendations	15d	03/17/25	04/04/25	152			03/17/25	04/04/25																								
154	Consolidate interim recommendations and findings	10d	04/07/25	04/18/25	153			04/07/25	04/18/25																								
155	Build Draft Report for public comment	10d	04/07/25	04/18/25	153			04/07/25	04/18/25																								
156	Approve Draft Report for public comment	5d	04/21/25	04/25/25	155			04/21/25	04/25/25																								
157	Publish Phase 2 Initial Report	0	04/25/25	04/25/25	156			04/25/25	04/25/25																								
158	Communicate Phase 2 Initial Report	5d	04/28/25	05/02/25	156			04/28/25	05/02/25																								
159	Public comment forum on Phase 2 Initial Report (40 days)	35d	04/28/25	06/13/25	156			04/28/25	06/13/25																								
160	FINAL REPORT	630d	06/12/23	11/07/25			Not Started	06/12/23	11/07/25																								
161	Phase 1 Final Report	105d	06/12/23	11/03/23				06/12/23	11/03/23																								
162	Review of public comments	30d	06/12/23	07/21/23	150			06/12/23	07/21/23																								
163	Continue deliberations of policy topics towards the Phase 1 Final Report	60d	07/24/23	10/13/23	162			07/24/23	10/13/23																								
164	Build Phase 1 Final Report & Final Deliberations	5d	10/16/23	10/20/23	163			10/16/23	10/20/23																								
165	Determine consensus levels on interim recommendations	10d	10/23/23	11/03/23	164			10/23/23	11/03/23																								
166	Adopt final recommendations and report	10d	10/23/23	11/03/23	164			10/23/23	11/03/23																								

Health	Category	Action Item	Priority	Assigned To	Baseline Finish	Current Finish	Status	Notes
	WP	ICANN75 - Session 1 TBD	↓	EPDP_IDN	09/17/22	09/17/22	Complete	
	WP	ICANN75 - Session 2 TBD	↓	EPDP_IDN	09/17/22	09/17/22	Complete	
	WP	Meeting #53 Project Plan and PCR, CQs D2 and D3	↓	EPDP_IDN	10/06/22	10/06/22	Complete	
	AI	Staff to send draft updated project plan and PCR to list, so that EPDP Team members can think about the options about provide input. This can also be discussed on the next call.	—	EPDP_IDN Leadership	10/13/22	10/13/22	Complete	
	AI	EPDP Team members to review draft communication officially requesting that Chinese, Japanese, and Korean GPs take on work regarding single character TLDs that are not allowed.	—	EPDP_IDN Leadership	10/13/22	10/13/22	Complete	
	AI	Staff to draft response to charter question A7 Part 2, indicating that this work will be outsourced to the GPs.	—	EPDP_IDN Leadership	11/03/22	10/19/22	Complete	
	AI	EPDP Team members to review the updates and confirm that the text is stable for recommendations under Charter Questions D2, D3.	—	EPDP_IDN	10/20/22	10/20/22	Complete	
	AI	Leadership team to follow up on list asking for additional positions on the string similarity approach.	—	EPDP_IDN Leadership	10/13/22	10/13/22	Complete	
	MS	Submit project package to GNSO Council	!	Ariel Liang	10/07/22	10/07/22	Complete	
	WP	Meeting #54 Project Plan and PCR, Rec 2.6, Hybrid Model	↓	EPDP_IDN	10/13/22	10/13/22	Complete	
	AI	EPDP Team members to respond on list about whether to do one Final Report or two Final Reports.	—	EPDP_IDN	10/20/22	10/20/22	Complete	
	AI	ALAC representatives to take into account RySG feedback on the proposed IG and provide additional feedback.	—	EPDP_IDN	10/27/22	10/27/22	Complete	
	WP	Meeting #55 D1b & B4	↓	EPDP_IDN	10/20/22	10/20/22	Complete	
●	AI	Leadership Team to develop draft recommendation in response to Charter Question D1b based on EPDP Team discussion.	—	EPDP_IDN Leadership	11/03/22		In Progress	
●	AI	Leadership Team to draft recommendation on discussion question 1 for Charter Question B4.	—	EPDP_IDN Leadership	11/03/22		In Progress	
	AI	In relation to discussion of Charter Question B4, staff to investigate the consequence on the process an applicant delegating a variant ahead of a primary.	—	Policy Support Staff	11/10/22		In Progress	
	WP	Meeting #56 B4, E2, E6	↓	EPDP_IDN	10/27/22	10/27/22	Complete	
	AI	Staff to follow up about which EPDP Team meetings may need to be cancelled in November and December.	—	Policy Support Staff	11/03/22	10/28/22	Complete	
	AI	EPDP members to provide input via mailing list on Charter Question E2 regarding the Legal Rights Objection. Staff to summarize key points for this discussion and Leadership to suggest a path forward.	—	EPDP_IDN Leadership EPDP_IDN Policy Support Staff	11/10/22		In Progress	
	AI	Leadership team to consider additional framing for the question at hand regarding Charter Question E2 for Community Objections and bring this back to the EPDP Team.	—	EPDP_IDN Leadership	11/10/22		In Progress	
	MS	Submit project package to GNSO Council	!	Ariel Liang	11/08/22		In Progress	
	WP	Meeting #57 TBD	↓	EPDP_IDN	11/10/22		In Progress	
	WP	Meeting #58 TBD	↓	EPDP_IDN	11/17/22		Not Started	
	WP	Meeting #59 Joint meeting w/ ccPDP4	↓	EPDP_IDN	11/29/22		Not Started	
	WP	Meeting #60 TBD	↓	EPDP_IDN	12/01/22		Not Started	
	WP	Meeting #61 TBD	↓	EPDP_IDN	12/08/22		Not Started	
	MS	Submit project package to GNSO Council	!	Ariel Liang	12/09/22		Not Started	
	WP	Meeting #62 TBD	↓	EPDP_IDN	12/15/22		Not Started	
	WP	Meeting #63 TBD	↓	EPDP_IDN	12/22/22		Not Started	
	MS	Submit project package to GNSO Council	!	Ariel Liang	01/06/23		Not Started	
	MS	Submit project package to GNSO Council	!	Ariel Liang	02/10/23		Not Started	
	MS	Submit project package to GNSO Council	!	Ariel Liang	03/10/23		Not Started	
	MS	Submit project package to GNSO Council	!	Ariel Liang	04/07/23		Not Started	
	MS	Submit Initial Report for Public Comment	!	EPDP_IDN	04/21/23		Not Started	
