


Project Tracking & Rollup DASHBOARD

Project Name Registration Data Accuracy Scoping Team **Program** **RDDS** **Project Sponsor** **GNSO Council**

Project Information

58%
Percent_Complete
07/12/21
Project_Start_Date
11/14/22
Project_End_Date


Tasks by Status

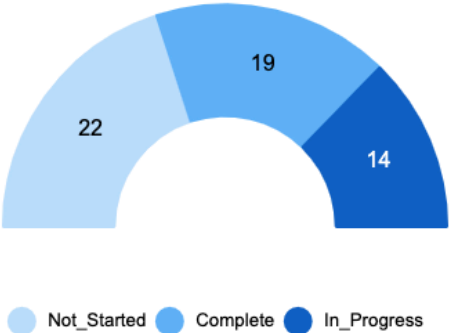

Project Contacts

Michael Palage
Chair
n/a
Vice_Chair
Olga Cavalli
Liaison
Marika Konings
Staff_Lead
Berry Cobb
Project_Manager

Participant Summary

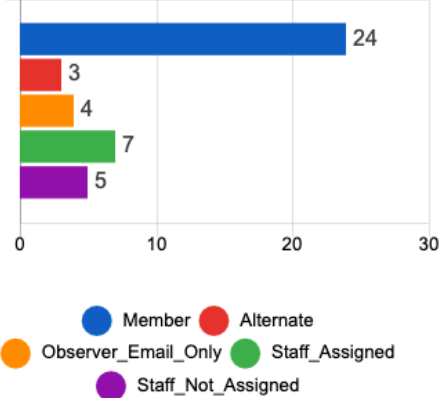

Project Status Health

Project_Status	Project_Health
On-Schedule	On-Target

Summary Gantt & Key Milestones

Health	Primary Task	Current Start	Current Finish	% Complete	Status	Timeline											
						2021				2022				2023			
						Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
	Registration Data Accuracy Scoping Team	07/12/21	11/14/22	58%	In Progress	Registration Data Accuracy Scoping Team											
	PROJECT CONTROL	07/12/21	11/14/22	70%	In Progress	PROJECT CONTROL											
	GROUP DELIBERATIONS	10/05/21	07/25/22	60%	In Progress	GROUP DELIBERATIONS											
●	Assignment 1 Enforcement and Reporting	10/19/21	01/24/22	99%	In Progress	Assignment 1 Enforcement and Reporting											
●	Assignment 2 Measurement of accuracy	10/19/21	01/24/22	89%	In Progress	Assignment 2 Measurement of accuracy											
●	Assignment 3 Effectiveness	01/25/22	05/02/22			Assignment 3 Effectiveness											
	Assignment 4 Impact and Improvements	05/03/22	07/25/22			Assignment 4 Impact and Improvements											
	FINAL REPORT	10/22/21	09/09/22	50%	In Progress	FINAL REPORT											
	Submission of Final Report to the GNSO Council	09/09/22	09/09/22			Submission of Final Report to the GNSO Council											

2 - Issue Scoping



Title:	Registration Data Accuracy Scoping Team (RDA_ST)
Description & Scope:	The GNSO Council adopted a proposal on 21 October 2020 which recommended that a Scoping Team address the effects of GDPR on Registration Data accuracy requirements and the Whois Accuracy Reporting System (ARS), stating, "a scoping team would be tasked to, 'facilitate community understanding of the issue; assist in scoping and defining the issue; gather support for the request of an Issue Report, and/or; serve as a means to gather additional data and/or information before a request [for an Issue Report] is submitted'. On 22 July 2021, the GNSO Council confirmed the formation of and instructions to the Accuracy Scoping Team. The Scoping Team will be tasked to consider a number of accuracy-related factors such as the current enforcement, reporting, measurement, and overall effectiveness of accuracy-related efforts. These considerations are expected to help inform its deliberations and the development of recommendations to the GNSO Council on whether any changes are recommended to improve accuracy levels, and, if so, how and by whom these changes would need to be developed (for example, if changes to existing contractual requirements are recommended, a PDP or contractual negotiations may be necessary to effect a change).







Composition:




Chair(s):	Michael Palage
Council Liaison:	Olga Cavalli
Policy Staff:	M. Konings, C. Tubergen, B. Cobb
GDS Staff	B. Gutterman
# Participants:	26 Participants (link)
# Observers:	9
Tools:	Mailing List / Meeting Schedule / Wiki
Charter:	N/A

Project Management:





Token Holder	Issue Start Date	Actual Start Date	# of Days	Planned End Date	Actual End Date
ST	21 Oct 2020	22 Jul 2021	266	11 Nov 2022	TBD

Program	Progress	Status	Health
RDDS	58%		

STATUS:  Planned  On-schedule  Revised schedule  Behind schedule  Target will be missed  On-hold

HEALTH:  On-Target  At-Risk  In-Trouble

Milestones/Work plan (link):

Milestone/Task	Date	
Project Start	Jul-21	✓
Scope Team Formation & Instructions	Jul-21	✓
1st Plenary meeting	Oct-21	✓
Project Plan and Work plan Adoption	Nov-21	✓
Address assignments 1	Jan-22	
Address assignments 2	Jan-22	
Address assignments 3	May-22	
Address assignments 4	Jul-22	
Send final recommendations to GNSO Council	Sep-22	
Prior period % Complete	50%	

Status/Health Rationale:

- This project was initiated on 22 Jul 2021 and continues with a Status of “On-Schedule” and Health of “On-Target”.

Current Activities:

- The team is continuing its deliberations on assignment #1 (Enforcement & Reporting) as well as assignment #2 (Measurement of Accuracy).
- Following an initial review of the input received from all groups on the gap analysis, the team continues to focus on how compliance with existing requirements can be measured as well as how perceived gaps can be documented and confirmed.
- In light of feedback received from ICANN Compliance, the team is in the process of finalizing the description of existing accuracy requirements and enforcement.

Planned Activities:

- All groups to finalize their input on how compliance with existing requirements can be measured.
- Scoping team to start deep diving into the different proposals to determine viability and required next steps.
- Share first draft of write up of assignment #1 deliberations with the Scoping Team.

Open Issues, Risks & Mitigation Plan:

- The Scoping team is behind the planned schedule for Assignments 1 & 2.

Completed in prior period(s):

- Completed and distributed [Project Package](#) for March.

Project Tracking & Rollup DASHBOARD




Project Roster


Participant	Participant Type	Role	Participation Start Date	Participation End Date	Legacy SOI Link
Group Selected / Nominated By: Group Name At-Large Advisory Committee (ALAC)					
Alan Greenberg	Member		09/23/21		https://community.icann.org
Group Selected / Nominated By: Group Name Commercial Business Users Constituency (BC)					
Susan Kawaguchi	Member		08/04/21		https://community.icann.org
Oluwatoba Obaniyi	Member		08/05/21		https://community.icann.org
Group Selected / Nominated By: Group Name GNSO Council					
Michael Palage	Member	Chair	09/23/21		https://community.icann.org
Olga Cavalli	Member	Liaison	11/03/21		https://community.icann.org
Group Selected / Nominated By: Group Name Governmental Advisory Committee (GAC)					
Velimira Nemiguentcheva-Grau	Member		09/02/21		https://community.icann.org
Melina Asimina Stroungi	Member		09/13/21		https://community.icann.org
Ryan Carroll	Member		09/15/21	04/01/22	https://community.icann.org
Kenneth Merrill	Member		12/15/21		https://community.icann.org
Group Selected / Nominated By: Group Name ICANN Board					
Becky Burr	Member	Liaison	11/18/21		https://community.icann.org
Harald Alvestrand	Alternate		12/08/21		https://community.icann.org
Group Selected / Nominated By: Group Name Intellectual Property Constituency (IPC)					
Lori Schulman	Member		09/02/21		https://community.icann.org
Scott R Austin	Member		09/02/21		https://community.icann.org
Group Selected / Nominated By: Group Name Internet Corporation for Assigned Names & Numbers (ICANN)					
Marika Konings	Staff - Assigned		07/22/21		
Berry Cobb	Staff - Assigned		07/22/21		
Terri Agnew	Staff - Assigned		07/22/21		
Nathalie Peregrine	Staff - Assigned		07/22/21		
Julie Bisland	Staff - Assigned		07/22/21		
Caitlin Tubergen	Staff - Assigned		07/22/21		
Devan Reed	Staff - Assigned		11/18/21		
Brian Gutterman	Member	Liaison	08/27/21		
Group Selected / Nominated By: Group Name Internet Service Providers and Connectivity Providers Constituency (ISPCP)					
Thomas Rickert	Member		11/04/21		https://community.icann.org
Group Selected / Nominated By: Group Name Non-Commercial Stakeholder Group (NCSG)					
Stephanie Perrin	Member		09/24/21		https://community.icann.org
Manju Chen	Member		09/24/21		https://community.icann.org
Group Selected / Nominated By: Group Name Registrar Stakeholder Group (RrSG)					
Sarah Wyld	Member		08/25/21		https://community.icann.org
Roger Carney	Member		08/25/21		https://community.icann.org
Volker Greimann	Member		08/26/21		https://community.icann.org
Owen Smigelski	Alternate		10/05/21		https://community.icann.org
Group Selected / Nominated By: Group Name Registry Stakeholder Group (RySG)					
Beth Bacon	Member		08/25/21		https://community.icann.org
Sophie Alice Hey	Member		08/25/21		https://community.icann.org
Marc Anderson	Member		08/30/21		https://community.icann.org
Alan Woods	Alternate		03/14/22		https://community.icann.org
Group Selected / Nominated By: Group Name Security and Stability Advisory Committee (SSAC)					
Steve Crocker	Member		08/25/21		https://community.icann.org
Jeff Bedser	Member		08/25/21	12/13/21	https://community.icann.org

Project Tracking & Rollup DASHBOARD


Work-Plan Activity Metrics

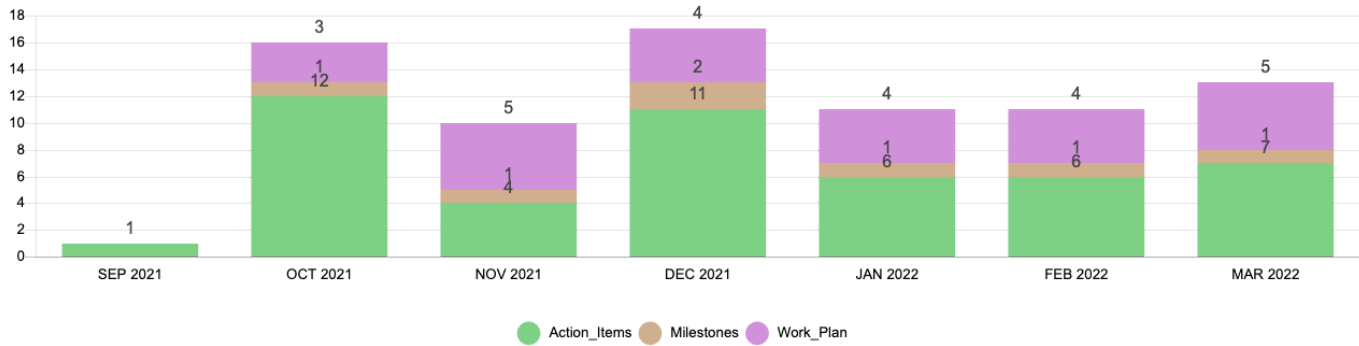

Mailman Activity

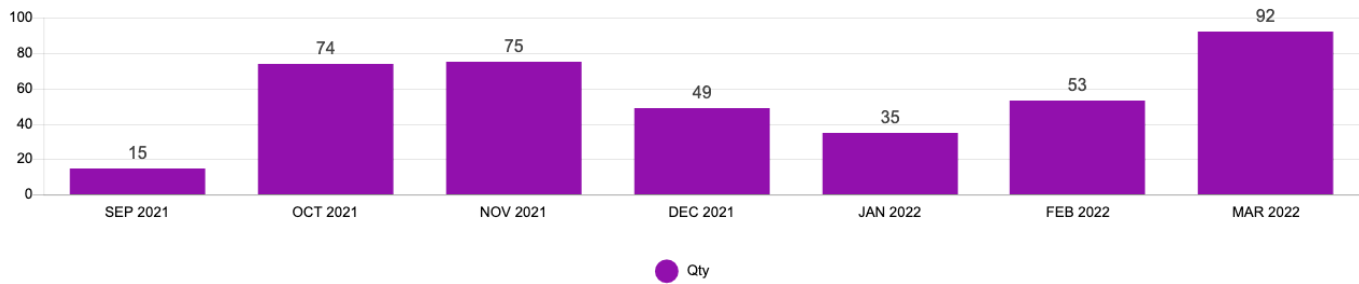

Meeting Activity

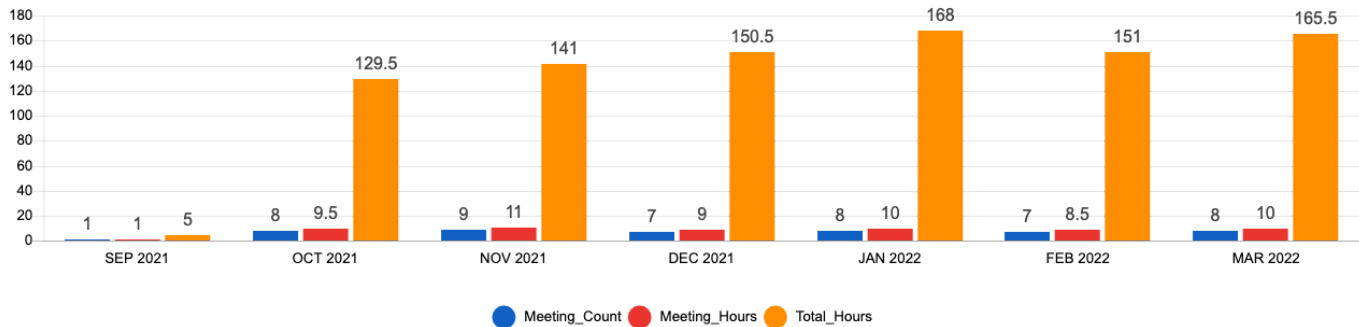

Plenary Attendance

Group Represented	Invited Qty	Attended Qty	Attendance
Total	Sum 568	Sum 442	Avg 77.8%
Primary At-Large Advisory Committee (ALAC)	Sum 24	Sum 22	Avg 91.7%
Attendee Name Alan Greenberg	Sum 24	Sum 22	Avg 91.7%
Primary Commercial Business Users Constituency (BC)	Sum 48	Sum 29	Avg 60.4%
Attendee Name Oluwatoba Obaniyi	Sum 24	Sum 9	Avg 37.5%
Attendee Name Susan Kawaguchi	Sum 24	Sum 20	Avg 83.3%
Primary GNSO Council	Sum 44	Sum 42	Avg 95.5%
Attendee Name Michael Palage	Sum 24	Sum 24	Avg 100.0%
Attendee Name Olga Cavalli	Sum 20	Sum 18	Avg 90.0%
Primary Governmental Advisory Committee (GAC)	Sum 85	Sum 48	Avg 56.5%

Attendee Name Kenneth Merrill	Sum 14	Sum 14	Avg 100.0%
Attendee Name Melina Asimina Stroungi	Sum 24	Sum 17	Avg 70.8%
Attendee Name Ryan Carroll	Sum 23	Sum 15	Avg 65.2%
Attendee Name Velimira Nemiguentcheva-Grau	Sum 24	Sum 2	Avg 8.3%
Primary ICANN Board	Sum 24	Sum 18	Avg 75.0%
Attendee Name Becky Burr	Sum 17	Sum 11	Avg 64.7%
Attendee Name Harald Alvestrand	Sum 7	Sum 7	Avg 100.0%
Primary Intellectual Property Constituency (IPC)	Sum 48	Sum 30	Avg 62.5%
Attendee Name Lori Schulman	Sum 24	Sum 16	Avg 66.7%
Attendee Name Scott R Austin	Sum 24	Sum 14	Avg 58.3%
Primary Internet Corporation for Assigned Names & Numbers (ICANN)	Sum 24	Sum 23	Avg 95.8%
Attendee Name Brian Gutterman	Sum 24	Sum 23	Avg 95.8%
Primary Internet Service Providers and Connectivity Providers Constituency (ISPCP)	Sum 20	Sum 15	Avg 75.0%
Attendee Name Thomas Rickert	Sum 20	Sum 15	Avg 75.0%
Primary Non-Commercial Stakeholder Group (NCSG)	Sum 48	Sum 42	Avg 87.5%
Attendee Name Manju Chen	Sum 24	Sum 22	Avg 91.7%
Attendee Name Stephanie Perrin	Sum 24	Sum 20	Avg 83.3%
Primary Registrar Stakeholder Group (RrSG)	Sum 88	Sum 80	Avg 90.9%
Attendee Name Owen Smigelski	Sum 16	Sum 14	Avg 87.5%
Attendee Name Roger Carney	Sum 24	Sum 21	Avg 87.5%
Attendee Name Sarah Wyld	Sum 24	Sum 22	Avg 91.7%
Attendee Name Volker Greimann	Sum 24	Sum 23	Avg 95.8%
Primary Registry Stakeholder Group (RySG)	Sum 74	Sum 67	Avg 90.5%
Attendee Name Alan Woods	Sum 2	Sum 2	Avg 100.0%
Attendee Name Beth Bacon	Sum 24	Sum 19	Avg 79.2%
Attendee Name Marc Anderson	Sum 24	Sum 23	Avg 95.8%
Attendee Name Sophie Alice Hey	Sum 24	Sum 23	Avg 95.8%
Primary Security and Stability Advisory Committee (SSAC)	Sum 41	Sum 26	Avg 63.4%
Attendee Name Jeff Bedser	Sum 17	Sum 6	Avg 35.3%
Attendee Name Steve Crocker	Sum 24	Sum 20	Avg 83.3%

[Open source report to view more](#)

Health	WBS	Task Name	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Status	Baseline Start	Baseline Finish	Q3			Q4			Q1			Q2			Q3								
											Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep						
1		Registration Data Accuracy Scoping Team	351d	07/12/21	11/14/22		58%	In Progress	07/12/21	11/14/22																					
2	1	PROJECT CONTROL	351d	07/12/21	11/14/22		70%	In Progress	07/12/21	11/14/22																					
3	1.1	Project start confirmed	9d	07/12/21	07/22/21		100%	Complete	07/12/21	07/22/21																					
4	1.2	Adopt/Confirm charter	0	07/22/21	07/22/21	3	100%	Complete	07/22/21	07/22/21																					
5	1.3	Confirmation of Team	55d	07/23/21	10/07/21	3	100%	Complete	07/23/21	10/07/21																					
6	1.4	Appointment of Team Chair	45d	07/23/21	09/23/21	3	100%	Complete	07/23/21	09/23/21																					
7	1.5	Appointment of Liaison to GNSO Council	55d	07/23/21	10/07/21	3	100%	Complete	07/23/21	10/07/21																					
8	1.6	Chair / Staff preparations	7d	09/24/21	10/04/21	6	100%	Complete	09/24/21	10/04/21																					
9	1.7	Project Management	297d	09/24/21	11/14/22		53%	In Progress	09/24/21	11/14/22																					
10	1.7.1	Develop and confirm Project Plan	21d	09/24/21	10/22/21	6	100%	Complete	09/24/21	10/22/21																					
11	1.7.2	Obtain project plan approval from GNSO Council	20d	10/25/21	11/19/21	10	100%	Complete	10/25/21	11/19/21																					
12	1.7.3	Develop monthly Project Packages and deliver to Group & Council	210d	11/22/21	09/09/22	11	44%	In Progress	11/22/21	09/09/22																					
13	1.7.4	Leadership Sub team	250d	09/24/21	09/08/22		54%	In Progress	09/24/21	09/08/22																					
14	1.7.4.1	On-going preparation and planning of group activities	250d	09/24/21	09/08/22	6	54%	In Progress	09/24/21	09/08/22																					
15	1.7.5	Close project and transition project to implementation	1d	11/14/22	11/14/22	14, 72			11/14/22	11/14/22																					
16	2	GROUP DELIBERATIONS	210d	10/05/21	07/25/22		60%	In Progress	10/05/21	07/25/22																					
17	2.1	First meeting of Team	1d	10/05/21	10/05/21	8	100%	Complete	10/05/21	10/05/21																					
18	2.2	Understand instructions, organize materials and develop initial approach	10d	10/05/21	10/18/21	8	100%	Complete	10/05/21	10/18/21																					
19	2.3	Overview & initial discussion of all assignments, review of index of resources	10d	10/05/21	10/18/21	8	100%	Complete	10/05/21	10/18/21																					
20	2.4	Develop and agree on working definitions and terminology	55d	10/05/21	12/20/21	8	100%	Complete	10/05/21	12/20/21																					
21	2.5	Assignment 1 Enforcement and Reporting	70d	10/19/21	01/24/22		99%	In Progress	10/19/21	01/24/22																					
22	2.5.1	Understand assignment and determine if any additional info is necessary	5d	10/19/21	10/25/21	18	100%	Complete	10/19/21	10/25/21																					
23	2.5.2	Assess measures used to monitor, measure, enforce and report on accuracy obligations	50d	10/26/21	01/03/22	22	100%	Complete	10/26/21	01/03/22																					
24	2.5.3	Develop draft work product	50d	10/26/21	01/03/22	22	100%	Complete	10/26/21	01/03/22																					
25	2.5.4	Conduct First Reading + verbal and email response	5d	01/04/22	01/10/22	24	100%	Complete	01/04/22	01/10/22																					
26	2.5.5	Conduct Second Reading + verbal response + adoption or discard	5d	01/11/22	01/17/22	25	90%	In Progress	01/11/22	01/17/22																					
27	2.5.6	Confirm draft as stable	5d	01/18/22	01/24/22	26	90%	In Progress	01/18/22	01/24/22																					
28	2.6	Assignment 2 Measurement of accuracy	70d	10/19/21	01/24/22		89%	In Progress	10/19/21	01/24/22																					
29	2.6.1	Understand assignment and determine need to deliberate	5d	10/19/21	10/25/21	18	100%	Complete	10/19/21	10/25/21																					
30	2.6.2	Deliberate on how accuracy levels can be determined and measured	50d	10/26/21	01/03/22	29	100%	Complete	10/26/21	01/03/22																					
31	2.6.3	Develop draft work product	50d	10/26/21	01/03/22	29	100%	Complete	10/26/21	01/03/22																					
32	2.6.4	Conduct First Reading + verbal and email response	5d	01/04/22	01/10/22	31	25%	In Progress	01/04/22	01/10/22																					
33	2.6.5	Conduct Second Reading + verbal response + adoption or discard	5d	01/11/22	01/17/22	32			01/11/22	01/17/22																					
34	2.6.6	Confirm draft as stable	5d	01/18/22	01/24/22	33			01/18/22	01/24/22																					
35	2.7	Assignment 3 Effectiveness	70d	01/25/22	05/02/22				01/25/22	05/02/22																					
36	2.7.1	Understand assignment and determine need to deliberate	5d	01/25/22	01/31/22	21, 28			01/25/22	01/31/22																					
37	2.7.2	On the basis of assignment 1 & 2, analyse accuracy levels measured to assess effectiveness of obligations	50d	02/01/22	04/11/22	36			02/01/22	04/11/22																					
38	2.7.3	Develop draft work product	50d	02/01/22	04/11/22	36			02/01/22	04/11/22																					
39	2.7.4	Conduct First Reading + verbal and email response	5d	04/12/22	04/18/22	38			04/12/22	04/18/22																					
40	2.7.5	Conduct Second Reading + verbal response + adoption or discard	5d	04/19/22	04/25/22	39			04/19/22	04/25/22																					
41	2.7.6	Confirm draft as stable	5d	04/26/22	05/02/22	40			04/26/22	05/02/22																					
42	2.8	Assignment 4 Impact and Improvements	60d	05/03/22	07/25/22				05/03/22	07/25/22																					
43	2.8.1	Understand assignment and determine need to deliberate	5d	05/03/22	05/09/22	35			05/03/22	05/09/22																					
44	2.8.2	On the basis of assignment 3, assess whether any changes are recommended and if so, how / by whom	40d	05/10/22	07/04/22	43			05/10/22	07/04/22																					
45	2.8.3	Develop draft work product	40d	05/10/22	07/04/22	43			05/10/22	07/04/22																					
46	2.8.4	Conduct First Reading + verbal and email response	5d	07/05/22	07/11/22	45			07/05/22	07/11/22																					
47	2.8.5	Conduct Second Reading + verbal response + adoption or discard	5d	07/12/22	07/18/22	46			07/12/22	07/18/22																					
48	2.8.6	Confirm draft as stable	5d	07/19/22	07/25/22	47			07/19/22	07/25/22																					
49	2.9	Unplanned Issues & Tasks	0	10/18/21	10/18/21				10/18/21	10/18/21																					
66	3	FINAL REPORT	231d	10/22/21	09/09/22		50%	In Progress	10/22/21	09/09/22																					
67	3.1	Combine findings and recommendations from assignments 1-4 into a Final Report	200d	10/22/21	07/28/22		58%	In Progress	10/22/21	07/28/22																					
68	3.2	Build Final Report & Final Deliberations	20d	07/29/22	08/25/22	67			07/29/22	08/25/22																					
69	3.3	Finalize Report	11d	08/26/22	09/09/22	68			08/26/22	09/09/22																					
70	3.4	Submission of Final Report to the GNSO Council	0	09/09/22	09/09/22	69			09/09/22	09/09/22																					
71	4	POST GROUP TASKS	45d	09/12/22	11/11/22			Not Started	09/12/22	11/11/22																					

Health	Category	Action Item	Priority	Assigned To	Baseline Finish	Current Finish	Status	Notes
67	WP	Meeting #19 - Measurement of Accuracy	↓	Scoping Team	02/24/22	02/24/22	Complete	
68	AI	RDA Scoping Team Members to review the definition/document provided by Staff Support (https://docs.google.com/document/d/1JGdNLjOjhmJnj-iDaGvcVnv1gZ5tQu5C/edit [docs.google.com]), which includes the Rr-provided accuracy definition augmented by the feedback from Contractual Compliance. Groups to include proposed edits or suggestions into the Google Doc by Wednesday, 2 March.	—	Scoping Team	03/02/22	03/17/22	In Progress	Extended due to confusion over assignment.
69	WP	Meeting #20 - Measurement of Accuracy	↓	Scoping Team	03/03/22	03/03/22	Complete	
70	AI	In advance of the ICANN73 RDA Scoping Team Session on Monday at 16:30 UTC, RDA Scoping Team Members to review the Gap Analysis Proposal Review. (https://docs.google.com/document/d/1sScP8MwgDCg4yvFNAYwQVqI7DQob60vX/edit) Note: this document was compiled by Support Staff in an effort to distill the proposals made by Scoping Team Members, including upsides and downsides noted by either the proposer or other team members in subsequent discussions. The document is not meant to restrict the group into choosing one proposal, but rather, the group should review all proposals and see which proposals provide a viable path to forward progress.	—	Scoping Team	03/07/22	03/07/22	In Progress	
71	MS	Submit project package	!	Leadership Team	03/04/22	03/04/22	Complete	
72	WP	Meeting ICANN73 - Review group's input on proposals	↓	Scoping Team	03/08/22	03/08/22	Complete	
73	AI	RDA Scoping Team Members to review their previous responses in light of the updated definition/document provided by Staff Support (https://docs.google.com/document/d/1JGdNLjOjhmJnj-iDaGvcVnv1gZ5tQu5C/edit [docs.google.com]), which focuses on current requirements and compliance. Groups to include proposed edits or suggestions into the Google Doc before the meeting on Thursday, 17 March.	—	Scoping Team	03/17/22	03/17/22	Complete	
74	AI	RDA Scoping Team Members to review the Gap Analysis Proposal Review. (https://docs.google.com/document/d/1sScP8MwgDCg4yvFNAYwQVqI7DQob60vX/edit) Note: this document was compiled by Support Staff in an effort to distill the proposals made by Scoping Team Members, including upsides and downsides noted by either the proposer or other team members in subsequent discussions. The document is not meant to restrict the group into choosing one proposal, but rather, the group should review all proposals and see which proposals provide a viable path to forward progress.	—	Scoping Team	03/17/22	03/17/22	Complete	
75	WP	Meeting #21 - Review Leadership's updated current state of accuracy and continue discussing Gap Analysis Proposal Review.	↓	Scoping Team	03/17/22	03/17/22	Complete	
76	AI	Brian Gutterman (ICANN org liaison) to transmit questions 3 - 7 (https://docs.google.com/document/d/1arKdQkRkE1LuurmDdd-PZP184_AdFm/edit?pli=1) to internal ICANN org colleagues for further guidance.	—	Brian Gutterman	03/24/22	03/23/22	Complete	Note: Responses expected in 3 weeks.
77	AI	Support Staff to provide further information on where the RDS WHOIS-2 Review Team recommendations, (specifically R 4.2, R 5.1, LE.1, CC.1) listed in the Data Analysis Proposals (https://docs.google.com/document/d/1arKdQkRkE1LuurmDdd-PZP184_AdFm/edit?pli=1) stand.	—	Policy Support Staff	03/23/22	03/23/22	Complete	
78	AI	RDA Scoping Team members to suggest further edits based on the discussion from today's meeting, including, for example, updated language regarding Spec. 13, to the current accuracy description: https://docs.google.com/document/d/1e5rUm-AFFDgNOU3OcT7ABu4InGwPiUyb/edit by Wednesday, 23 March.	—	Scoping Team	03/23/22	03/23/22	Complete	
79	AI	Still open: In advance of the next meeting on Thursday, 24 March, RDA Scoping Team Members to review the Gap Analysis Proposal Review. (https://docs.google.com/document/d/1sScP8MwgDCg4yvFNAYwQVqI7DQob60vX/edit) Note: this document was compiled by Support Staff in an effort to distill the proposals made by Scoping Team Members, including upsides and downsides noted by either the proposer or other team members in subsequent discussions. The document is not meant to restrict the group into choosing one proposal, but rather, the group should review all proposals and see which proposals provide a viable path to forward progress. Note: IPC Reps: please respond to the comments directed to you in Proposal H.	—	Scoping Team	03/23/22		In Progress	Still outstanding: Note: IPC Reps: please respond to the comments directed to you in Proposal H.
80	WP	Meeting #22 - Review Leadership's updated current state of accuracy and continue discussing Gap Analysis Proposal Review.	↓	Scoping Team	03/24/22	03/24/22	Complete	
81	AI	Scoping Team members to review the updates to the Accuracy working description and propose FINAL edits by Wednesday, 30 March. Support Staff will lock the document after the deadline.	—	Scoping Team	03/30/22	03/30/22	Complete	
82	AI	Scoping Team members to consider the Gap Analysis and specifically review the "next steps" column of each proposal by Wednesday, 30 March. The group will begin by discussing the potential next steps for Proposal A during the next meeting on 31 March, so please come prepared for this discussion.	—	Scoping Team	03/30/22	03/30/22	Complete	
83	WP	Meeting #23 - Gap Analysis Deeper Dive (next steps)	↓	Scoping Team	03/31/22	03/31/22	Complete	
84	AI	Scoping Team to continue deep dive review into the Gap Analysis proposals (beginning on p. 8 of Google Doc) to identify relevant mitigation to noted downsides and next steps (by whom, by when, additional considerations) by Wednesday, 6 April.	—	Scoping Team	04/06/22		In Progress	
85	AI	Michael P. to confirm, via the list, if/how to proceed with respect to a potential small team for Proposal A (registrar survey) by Monday, 4 April.	—	Michael Palage	04/04/22		In Progress	
86	AI	Scoping Team Members to review the updates to the current description of accuracy requirements and enforcement and try to resolve outstanding issues on the list among the interested members/conflicting opinions by COB Wednesday, 6 April.	—	Scoping Team	04/06/22		In Progress	
87	WP	Meeting #24 TBD	↓	Scoping Team	04/07/22		In Progress	
88	MS	Submit project package	!	Leadership Team	04/08/22		In Progress	
89	WP	Meeting #25 TBD	↓	Scoping Team	04/14/22		Not Started	
90	WP	Meeting #26 TBD	↓	Scoping Team	04/21/22		Not Started	
91	WP	Meeting #27 TBD	↓	Scoping Team	04/28/22		Not Started	
92	MS	Submit project package	!	Leadership Team	05/05/22		Not Started	
93	WP	Meeting #28 TBD	↓	Scoping Team	05/05/22		Not Started	
94	WP	Meeting #29 TBD	↓	Scoping Team	05/12/22		Not Started	
95	WP	Meeting #30 TBD	↓	Scoping Team	05/19/22		Not Started	
96	WP	Meeting #31 TBD	↓	Scoping Team	05/26/22		Not Started	
97	WP	Meeting #32 TBD	↓	Scoping Team	06/02/22		Not Started	
98	MS	Submit project package	!	Leadership Team	06/07/22		Not Started	
99	WP	Meeting #33 TBD	↓	Scoping Team	06/09/22		Not Started	
100	WP	Meeting ICANN74 TBD	↓	Scoping Team	06/14/22		Not Started	
101	MS	Deliver Report to GNSO Council	!	Leadership Team	09/11/22		Not Started	
