

Project Tracking & Rollup DASHBOARD

Project Name EPDP: Internationalized Domain Names **Program** IDNs **Project Sponsor** GNSO Council

Project Information

71%
% Complete

05/20/21
Actual Start

02/21/25
Planned Finish

Tasks by Status

Project Contacts

Donna Austin
Chair

Justine Chew
Vice_Chair

Farell Folly
Liaison

Ariel Liang
Staff_Lead

Steve Chan
Project_Manager

Participant Summary

Project Status & Health

Project_Status	Project_Health
Revised Schedule	On-Target

Summary Gantt & Key Milestones

Health	Primary Task	Current Start	Current Finish	% Complete	Status	2021	2022	2023	2024	2025								
						Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1
	EPDP: Internationalized Domain Names	05/20/21	02/21/25	71%	In Progress	[Gantt Bar]												
	PROJECT CONTROL	05/20/21	01/13/25	72%	In Progress	[Gantt Bar]												
	GROUP DELIBERATIONS	08/11/21	06/13/24	77%	In Progress	[Gantt Bar]												
	Group 1: Definition of All gTLDs Using RZ-LGR	08/25/21	02/17/22	100%	Complete	[Gantt Bar]												
	Group 2: Same Entity at Top-Level	02/04/22	03/31/22	100%	Complete	[Gantt Bar]												
	Group 3: Objection Processes, String Similarity Review, String Contention Resolution, Reserved Strings, and Other Policies and Procedures as Impacted by Variants	03/18/22	01/06/23	100%	Complete	[Gantt Bar]												
	Data Collection to Facilitate Phase 2 Deliberations	11/07/22	07/07/23	100%	Complete	[Gantt Bar]												
	Group 4: Same Entity at Second-Level	11/10/23	12/21/23	83%	In Progress	[Gantt Bar]												
	Group 5: Domain Name Lifecycle	11/10/23	01/18/24	47%	In Progress	[Gantt Bar]												
	Group 6: Registration Dispute Resolution Procedures and Trademark Protection Mechanisms	11/10/23	01/25/24	11%	In Progress	[Gantt Bar]												
	Group 7: IDN Implementation Guidelines	01/12/24	02/29/24	18%	In Progress	[Gantt Bar]												
	INITIAL REPORT	09/20/21	05/31/24	84%	In Progress	[Gantt Bar]												
	Publish Phase 1 Initial Report	04/21/23	04/21/23	100%	Complete	[Gantt Bar]												
	Public comment forum on Phase 1 Initial Report (56 calendar days)	04/24/23	06/19/23	100%	Complete	[Gantt Bar]												
	Publish Phase 2 Initial Report	04/19/24	04/19/24		Not Started	[Gantt Bar]												
	Public comment forum on Phase 2 Initial Report (40 calendar days)	04/22/24	05/31/24		Not Started	[Gantt Bar]												
	FINAL REPORT	06/20/23	10/11/24	45%	In Progress	[Gantt Bar]												
	Review of public comments - Phase 1	06/20/23	09/11/23	100%	Complete	[Gantt Bar]												
	Submission of Phase 1 Final Report to the GNSO Council	11/09/23	11/09/23		Not Started	[Gantt Bar]												
	Review of public comments - Phase 2	06/03/24	08/23/24		Not Started	[Gantt Bar]												
	Submission of Phase 2 Final Report to the GNSO Council	10/11/24	10/11/24		Not Started	[Gantt Bar]												
	POST GROUP TASKS	10/14/24	02/21/25		Not Started	[Gantt Bar]												
	Approval of Final Report and Recommendations by the GNSO Council	10/14/24	12/13/24		Not Started	[Gantt Bar]												
	Publish Recommendations for Public Comment for Board consideration	01/06/25	02/21/25		Not Started	[Gantt Bar]												

Project Description

On 20 May 2021, the GNSO Council passed a resolution to initiate the Expedited Policy Development Process (EPDP) on Internationalized Domain Names and adopt its charter. The EPDP Team is tasked with providing the GNSO Council with policy recommendations on: 1) the definition of gTLDs and the management of variant labels; and 2) how the IDN Implementation Guidelines, which Contracted Parties are required to comply with, should be updated in the future.

- [Mailing List](#)
- [Meeting Schedule](#)
- [Wiki](#)
- [Charter](#)

Open Issues & Risks

- Deliberations of certain charter questions dependent upon input from external parties.

Completed in Prior Period

- Finalized all Phase 1 final recommendations.
- Completed and distributed [Project Package](#).

Current Activities & Tasks

- Conducting consensus call on Phase 1 final recommendations.
- Finalizing Phase 1 Final Report.
- Conducting second reading of draft recommendations related to Phase 2 charter questions that the EPDP Team completed initial deliberations on.
- Conducting Phase 2 charter question deliberations, which includes conducting three working sessions at ICANN78.

Planned Activities & Tasks



- Plan for the dedicated face-to-face workshop in December 2023.

Work-Plan Activity Metrics



Mailman Activity



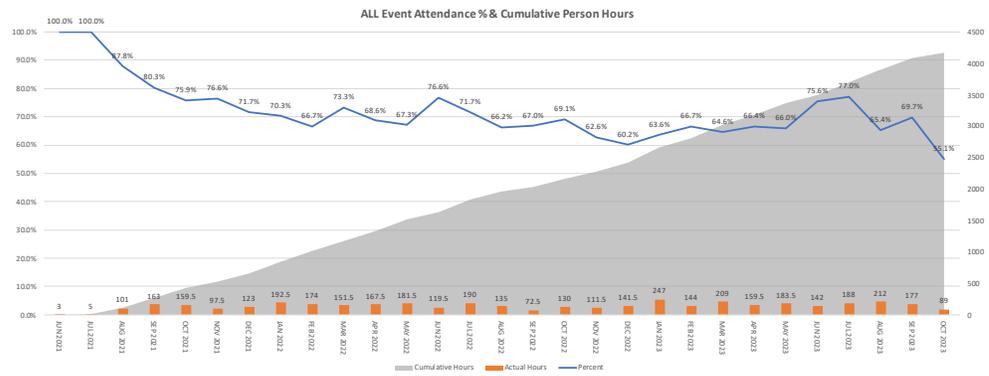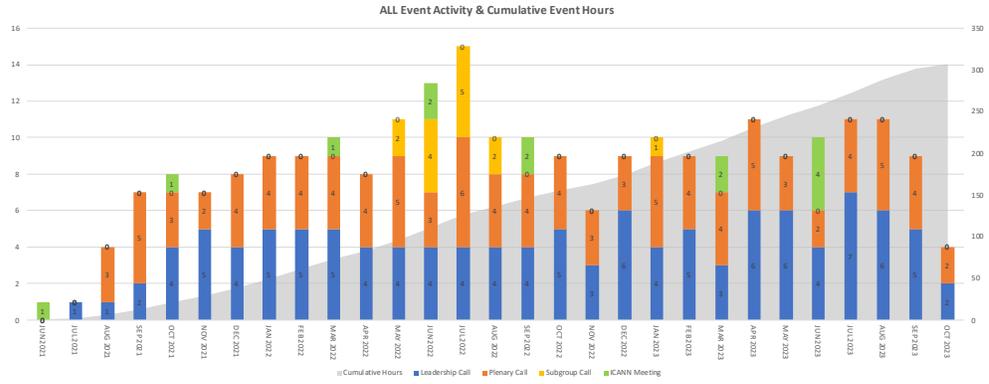

Plenary Roster and Attendance Only

Row Labels	Sum of Invited Qty	Sum of Attended Qty	Percent	Role	SOI	Start Date	Depart Date
Participant	1048	436	41.6%				
At-Large Advisory Committee (ALAC)	320	101	31.6%				
Justine Chew	95	95	99.0%	Vice-chair	https://community.icann.org/v/TeAg	5/25/2021	
TV Gopal	24	6	25.0%		https://community.icann.org/v/ByTSCG	5/25/2021	3/21/2022
Independent	657	184	28.0%				
Abdilmontem Gallia	90	5	5.6%		https://community.icann.org/v/20J6CQ	5/25/2021	
Nabil Benamar	89	0	0.0%		https://community.icann.org/v/3wTpcQ	5/25/2021	
Anil Jain	91	65	71.4%		https://community.icann.org/v/1P8CQ	7/30/2021	
Quoc Pham	88	12	13.6%		https://community.icann.org/v/G2bAw	8/13/2021	
Imran Hosen	59	13	22.0%		https://community.icann.org/v/L9MGCw	11/4/2021	
Wael Nasr	54	0	0.0%		https://community.icann.org/v/8B4D	5/9/2022	
Lei Gao	89	1	1.1%		https://community.icann.org/v/4QDPCQ	5/25/2021	
Shuo Liang	91	84	92.3%		https://community.icann.org/v/2wT6CQ	5/25/2021	
Abdulnadir Roba	6	4	66.7%			8/22/2023	
Registry Stakeholder Group (RySG)	181	90	49.7%				
Jerry Son	91	87	95.6%		https://community.icann.org/v/ANX8CQ	5/25/2021	
Wei (Wesley) Wang	90	3	3.3%		https://community.icann.org/v/YNP8CQ	7/13/2021	
Governmental Advisory Committee (GAC)	90	61	67.8%				
Hamza Onoruoiza Salami	81	57	70.4%		https://community.icann.org/v/4E8CQ	5/25/2021	7/20/2023
Amna Ramallan	9	4	44.4%		https://community.icann.org/v/RI0CQg	7/20/2023	
Member	1723	1179	68.4%				
At-Large Advisory Committee (ALAC)	275	243	88.4%				
Satish Babu	92	82	89.1%		https://community.icann.org/v/RLrAw	5/25/2021	
Abdulkarim Oloyede	91	75	82.4%		https://community.icann.org/v/Y02Bg	5/25/2021	
Hadia Elmimawi	92	86	93.5%		https://community.icann.org/v/kwDRaw	7/14/2021	
Commercial Business Users Constituency (BC)	34	2	5.9%				
Mark William Datsygold	34	2	5.9%		https://community.icann.org/v/Pwb0C	5/25/2021	5/12/2022
GNSO Council	195	159	81.5%				
Donna Austin	103	98	95.1%	Chair	https://community.icann.org/v/7tBEAg	8/10/2021	
Fareh Foty	92	61	66.3%	Liason	https://community.icann.org/v/35tAw	7/27/2021	
Intellectual Property Constituency (IPC)	104	46	44.2%				
Brian King	13	10	76.9%		https://community.icann.org/v/054F8D	5/25/2021	11/8/2021
Jeffrey Neuman	91	36	39.6%		https://community.icann.org/v/guBwAg	5/25/2021	
Internet Service Providers and Connectivity Providers Constituency (ISPCP)	103	44	42.7%				
Christian Dawson	90	33	36.7%		https://community.icann.org/v/2vV6Ag	7/12/2021	
Nitin Walia	13	11	84.6%		https://community.icann.org/v/8ob3Dg	5/31/2023	
Non-Commercial Stakeholder Group (NCSG)	152	42	27.6%				
Taiwo Akinremi	91	14	15.4%		https://community.icann.org/v/3vqu8e	7/15/2021	
Grace Githiga	9	0	0.0%		https://community.icann.org/v/h4tDg	7/26/2023	
Emmanuel Eliot Agbenonwoosi	52	28	53.8%		https://community.icann.org/v/H44zCg	7/13/2022	
Registrar Stakeholder Group (RySG)	177	158	89.3%				
Michael Bauland	92	79	85.9%		https://community.icann.org/v/Yww0CQ	5/25/2021	
Duowei Chen	16	11	68.8%		https://community.icann.org/v/LQ8HAg	9/26/2021	2/13/2022
Zhang Zuan	69	68	98.6%		https://community.icann.org/v/7p06Ag	2/14/2022	
Registry Stakeholder Group (RySG)	346	283	81.8%				
Maksim Alzobas	91	73	80.3%		https://community.icann.org/v/8TtV8Ag	5/25/2021	
Dennis Tan Tanaka	91	85	93.4%		https://community.icann.org/v/14tF8Ag	5/25/2021	
Jennifer Chung	90	66	73.3%		https://community.icann.org/v/6A0uAg	5/25/2021	
Joseph Chiu-Kit Yee	74	59	79.7%		https://community.icann.org/v/5Y88CQ	7/6/2021	5/2/2023
Governmental Advisory Committee (GAC)	182	73	40.1%				
Nigel Hickson	91	52	57.1%		https://community.icann.org/v/94P8CQ	7/12/2021	
SANTHOSH THAMPY	91	21	23.1%		https://community.icann.org/v/7ZrAw	5/25/2021	
ICANN Board	155	129	83.2%				
Edmon Chung	95	79	83.2%	Liason	https://community.icann.org/v/25WwAw	7/27/2021	
Alinori Abejura	36	29	80.6%	Liason	https://community.icann.org/v/4t4DCg	11/18/2021	
Alan Barrett	24	21	87.5%	Liason	https://community.icann.org/v/0P5DQ	3/16/2023	
Grand Total	2771	1615	58.3%				

Staff Support Roster

Row Labels	Start Date	Depart Date
Internet Corporation for Assigned Names & Numbers (ICANN)		
Dewan Reed	12/2/2021	
Emily Barabas	5/25/2021	7/18/2023
Terri Agnew	5/25/2021	
Steve Chan	5/25/2021	
Anil Liang	5/25/2021	
Michael Karakash	5/25/2021	
Sarmad Hussain	5/25/2021	
Pitinan Koamornratpana	5/25/2021	
Julia Bisland	5/25/2021	

Health	Task Name	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Status	2021				2022				2023				2024				2025			
								Q1	Q2	Q3	Q4																
1	EPDP: Internationalized Domain Names	982d	05/20/21	02/21/25		71%	In Progress																				
2	PROJECT CONTROL	953d	05/20/21	01/13/25		72%	In Progress																				
3	Project start confirmed	0	05/20/21	05/20/21		100%	Complete																				
4	Adopt/Confirm charter	0	05/20/21	05/20/21	3	100%	Complete																				
5	Confirmation of Team	60d	05/20/21	08/11/21	3	100%	Complete																				
6	Appointment of Team Chair	46d	05/20/21	07/22/21	3	100%	Complete																				
7	Appointment of Liaison to GNSO Council	46d	05/20/21	07/22/21	3	100%	Complete																				
8	Chair / Staff preparations	13d	07/23/21	08/10/21	6	100%	Complete																				
9	Project Management	907d	07/23/21	01/13/25		67%	In Progress																				
10	Develop and confirm Project Plan	50d	07/23/21	09/30/21	6	100%	Complete																				
11	Obtain project plan approval from GNSO Council	20d	10/01/21	10/28/21	10	100%	Complete																				
12	Develop monthly Project Packages and deliver to Group & Council	789d	10/29/21	11/06/24	11	65%	In Progress																				
13	Leadership Sub team	869d	07/23/21	11/20/24		67%	In Progress																				
14	On-going preparation and planning of group activities	869d	07/23/21	11/20/24	6	67%	In Progress																				
15	Close project and transition project to implementation	1d	01/13/25	01/13/25	14, 177	0%																					
16	GROUP DELIBERATIONS	742d	08/11/21	06/13/24		77%	In Progress																				
17	First meeting of Team	1d	08/11/21	08/11/21	8	100%	Complete																				
18	Understand Charter, organize materials and develop initial approach	10d	08/11/21	08/24/21	8	100%	Complete																				
19	Overview & initial discussion of all Policy Topics	10d	08/11/21	08/24/21	8	100%	Complete																				
20	Develop definitions and terminology	28d	08/11/21	09/17/21	8	100%	Complete																				
21	+ Input from other SO/ACs & GNSO SG/Cs	58d	09/09/21	11/29/21		100%	Complete																				
26	- Phase 1 Deliberations	403d	08/25/21	03/10/23		100%	Complete																				
27	+ Group 1: Definition of All gTLDs Using RZ-LGR	127d	08/25/21	02/17/22		100%	Complete																				
44	+ Group 2: Same Entity at Top-Level	40d	02/04/22	03/31/22		100%	Complete																				
58	+ Group 3: Objection Processes, String Similarity Review, String Contention Resolution, Reserved Strings, and Other Policies and Procedures as Impacted by Variants	211d	03/18/22	01/06/23		100%	Complete																				
75	Review ICANN Org Input for Phase 1 Draft Recommendations	55d	12/26/22	03/10/23	72	100%	Complete																				
76	Data Collection to Facilitate Phase 2 Deliberations	175d	11/07/22	07/07/23		100%	Complete																				
77	- Phase 2 Deliberations	234d	05/01/23	03/21/24		44%	In Progress																				
78	Preliminary deliberations for Phase 2 Charter Questions (C1, C2, C4, C4a, C5, C6, D4, D6, D7)	36d	05/01/23	06/19/23	147	100%	Complete																				
79	+ Group 4: Same Entity at Second-Level	30d	11/10/23	12/21/23		83%	In Progress																				
93	+ Group 5: Domain Name Lifecycle	50d	11/10/23	01/18/24		47%	In Progress																				
108	+ Group 6: Registration Dispute Resolution Procedures and Trademark Protection Mechanisms	55d	11/10/23	01/25/24		11%	In Progress																				
118	+ Group 7: IDN Implementation Guidelines	35d	01/12/24	02/29/24		18%	In Progress																				
127	Review ICANN Org Input for Phase 2 Draft Recommendations	15d	03/01/24	03/21/24	126	0%																					
128	+ Key Group Events	689d	10/25/21	06/13/24		66%	In Progress																				
139	INITIAL REPORT	705d	09/20/21	05/31/24		84%	In Progress																				
140	+ Phase 1 Initial Report	456d	09/20/21	06/19/23		100%	Complete																				
149	- Phase 2 Initial Report	141d	11/17/23	05/31/24		32%	In Progress																				
150	Populate stable drafts as required	95d	11/17/23	03/28/24	81	50%	In Progress																				
151	Discuss/approve findings and interim recommendations	1d	03/29/24	03/29/24	150																						
152	Consolidate interim recommendations and findings	1d	04/01/24	04/01/24	151																						
153	Build Draft Report for public comment	10d	04/01/24	04/12/24	151																						
154	Approve Draft Report for public comment	5d	04/15/24	04/19/24	153																						
155	Publish Phase 2 Initial Report	0	04/19/24	04/19/24	154																						
156	Communicate Phase 2 Initial Report	5d	04/22/24	04/26/24	154																						
157	Public comment forum on Phase 2 Initial Report (40 calendar days)	30d	04/22/24	05/31/24	154																						
158	FINAL REPORT	344d	06/20/23	10/11/24		45%	In Progress																				
159	- Phase 1 Final Report	103d	06/20/23	11/09/23		86%	In Progress																				
160	Review of public comments - Phase 1	60d	06/20/23	09/11/23	148	100%	Complete																				
161	Continue deliberations of policy topics towards the Phase 1 Final Report	80d	06/20/23	10/09/23	148	100%	Complete																				
162	Build Phase 1 Final Report & Final Deliberations	10d	10/10/23	10/23/23	161	100%	Complete																				
163	Determine consensus levels on interim recommendations	13d	10/24/23	11/09/23	162	10%	In Progress																				

Health	Category	Action Item	Priority	Assigned To	Baseline Finish	Current Finish	Status	Notes
	WP	Meeting #94 Review of Proposed Updates of Phase 1 Final Recommendations	↓	EPDP_IDN	08/31/23	08/31/23	Complete	
	AI	Leadership will look to set an agenda for the F2F Workshop in December as to allow representative groups time to discuss and strategize for the meeting	—	EPDP_IDN Leadership	11/17/23		In Progress	
	AI	Leadership will reconsider Recommendation 3.xx for further clarification	—	EPDP_IDN Leadership	09/21/23	09/21/23	Complete	
	AI	Leadership will work to re-write Rec. 3.5.4. to better address the responsibilities of the registry operator in relation to the end-user.	—	EPDP_IDN Leadership	09/21/23	10/05/23	Complete	
	AI	Leadership will discuss the wording of 3.5.1 and determine if the second part of the statement is redundant due to the definition of variant.	—	EPDP_IDN Leadership	09/21/23	10/05/23	Complete	
	AI	The ALAC will review the updated language in Rec 3.5 and IG 3.6	—	Abdulkarim Oloyede Hadia Elminiawi Satish Babu	09/21/23	09/21/23	Complete	
	AI	The team will deliberate on IG 3.9 and how to proceed with the specifics of the application process	—	EPDP_IDN	09/21/23	09/21/23	Complete	
	WP	Meeting #95 Review of Proposed Updates of Phase 1 Final Recommendations	↓	EPDP_IDN	09/07/23	09/07/23	Complete	
	MS	Submit project package to GNSO Council	!	Ariel Liang	09/11/23	09/11/23	Complete	
	WP	Meeting #96 --Cancelled--	↓	EPDP_IDN	09/14/23	09/14/23	Complete	
	WP	Meeting #97 Rec 3.5, IG 3.6, Rec 4.4	↓	EPDP_IDN	09/21/23	09/21/23	Complete	
	AI	The chair asked registries and registrars to work on Rec 3.5.4 by next week, including having a discussion together with the ALAC after they finish their review, to find potential solutions to this recommendation item.	—	EPDP_IDN Leadership	09/28/23	09/28/23	Complete	
	AI	The registries and registrars will also work on reviewing and potentially proposing updated language for I.G. 3.6 by next week.	—	EPDP_IDN	09/28/23	09/28/23	Complete	
	AI	The team will review the proposed Rec 4.4 for discussion next week.	—	EPDP_IDN	09/28/23	09/28/23	Complete	
	WP	Meeting #98 Rec 3.5, IG 3.6, Rec 4.4; selected sections of P1 Final Report	↓	EPDP_IDN	09/28/23	09/28/23	Complete	
	AI	The ALAC proposed language for 3.5 will be adopted, pending review by the RySG, with a possibility of further revisions over the use of "resellers" in the new 3.5.4.	—	Ariel Liang	10/05/23	10/05/23	Complete	
	AI	The team members will take the ALAC proposed language for IG 3.6 back to their stakeholder groups for review by the next meeting on 5 October. If there are no discrepancies, the ALAC IG 3.6 will be adopted.	—	EPDP_IDN	10/05/23	10/05/23	Complete	
	AI	The Leadership proposed Rec 4.4 was approved unanimously by the EPDP team.	—	Ariel Liang	09/28/23	09/28/23	Complete	
	AI	The P1 Final report will be made available by ICANN Staff to the EPDP team for their review, with sections 1,3, and 5 needing input. The rest will not need input as they remain largely uncontroversial (administrative / procedural). The Chair requests review to be completed by Meeting #99 on 5 October.	—	Ariel Liang	10/05/23	10/05/23	Complete	
	AI	The team will use "recommendation" with a lowercase r in their final report.	—	Ariel Liang	09/28/23	09/28/23	Complete	
	WP	Meeting #99 Rec 3.5, IG 3.6, Rec 4.4; Phase 2 refresher + second reading of draft recs	↓	EPDP_IDN	10/05/23	10/05/23	Complete	
	AI	The Team will review Rationale for Rec 3.5 and IG 3.6 by next week's meeting, Meeting #100, on 12 October.	—	EPDP_IDN	10/12/23	10/12/23	Complete	
	AI	The Team will review the updates to Rec 4.4 by next week's meeting, Meeting #100, on 12 October.	—	EPDP_IDN	10/12/23	10/12/23	Complete	
	AI	Staff will begin the consensus call process for all resolved recommendations (i.e., excluding Rec 4.4 if not agreed to by 12 October)	—	Ariel Liang	10/12/23	10/12/23	Complete	
	WP	Meeting #100 Rec 3.5, IG 3.6, Rec 4.4; second reading of Phase 2 draft recs	↓	EPDP_IDN	10/12/23	10/12/23	Complete	
	MS	Submit project package to GNSO Council	!	Ariel Liang	10/15/23	10/15/23	Complete	
	WP	ICANN78 - Session 1 Source Domain, Same Registrant, Domain Transaction Fees	↓	EPDP_IDN	10/21/23		In Progress	
	WP	ICANN78 - Session 2 Source Domain, Same Registrant, Domain Transaction Fees	↓	EPDP_IDN	10/21/23		In Progress	
	WP	ICANN78 - Session 3 Source Domain, Same Registrant, Domain Transaction Fees	↓	EPDP_IDN	10/23/23		In Progress	
	WP	Meeting #101 TBD	↓	EPDP_IDN	11/02/23		In Progress	
	MS	Submit project package to GNSO Council	!	Ariel Liang	11/06/23	10/15/23	Complete	Given short duration between ICANN78 and Nov Council, a package will not be created.
	MS	Submission of Phase 1 Final Report to the GNSO Council	!	EPDP_IDN	11/03/23		In Progress	
	MS	Submit project package to GNSO Council	!	Ariel Liang	12/11/23		Not Started	
